

# MEASURE L BOND UPDATE

September 12, 2017

### Measure L – Overview

- Phase 2 Project Update
- Phase 3 Project Update
- Phase 4 Project Update
- Program Schedule Review

## Measure L – Phase 2 Projects

### Vinci Park Elementary School - FIS

- FIS drawing are at DSA for review. Anticipate approval by mid-September.
- Bids late September 2017
- Start construction late October 2017
- Exterior Canopy
  - Submit to CGS (California Geological Survey) mid September (3 month review time)
  - DSA December 2017
  - Purchase/install January/February 2018
- Completion February 2018

#### FIS Furniture

- Meeting with Principal August/September
- Order furniture by early November 2017
- Furniture delivery mid February 2018

- Student Nutrition moved into the new office space on 7.26.17
- Central Kitchen was open to the public on 8.1.17
- Received Final Health Department approval on 8.10.17
- Contractor is working on completing Punch List Items

## Measure L – Phase 3 Projects

### Laneview Modernization Projects

- Punch List items anticipated completion early September
- Glazing (exterior glass replacement) scheduled to be completed by 9/30 (weekend work)

### Majestic Way Modernization Project

- Punch List items anticipated completion late September
- Glazing (exterior glass replacement) scheduled to be completed by 10/8 (weekend work)

### Ruskin Modernization Project

- Punch List items anticipated completion late September
- Glazing (exterior glass replacement) schedule to be completed by 9/17 (weekend work)

### Piedmont Modernization Project

- Punch List items anticipated completion late September
- Glazing (exterior glass replacement) schedule to be completed by 9/30 (weekend work)

# Laneview Elementary School




# Laneview Elementary School









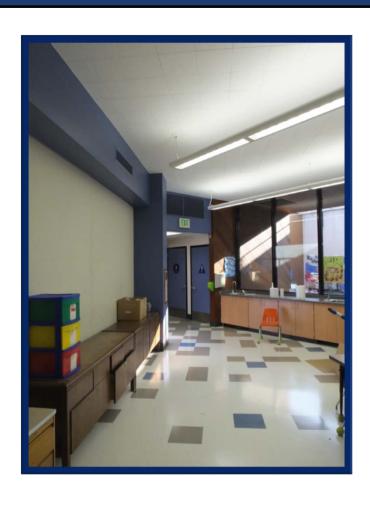



# Ruskin Elementary School



# Ruskin Elementary School



# Ruskin Elementary School

















### Measure L – Phase 3 Projects

### Modernization Projects

- Moving
  - Moves were completed by August 9, 2017
  - Contractor is currently replacing missing or damaged items
- Furniture Classroom
  - Installation was completed by August 11, 2017
  - Vendor is completing Punch List items
- Pavement Rehabilitation
  - The paving projects at Brooktree, Majestic Way, and Cherrywood are complete
- Pavement Rehabilitation Piedmont Middle School
  - Design to be complete by 9/30
  - District review early October 2017
  - Submit to City & DSA for review mid October 2017
  - Bid early February 2018
  - Construction starts June 2018

## Measure L – Phase 3 Projects

### Laneview FIS Project

- Bids September 19, 2017
- Start construction late October 2017
- Completion February 2018

### Majestic Way FIS Project

- Bids September 19, 2017
- Start construction late October 2017
- Completion February 2018


#### FIS Furniture


- Vendor meeting with site Principals August/September 2017
- Order furniture by early November 2017
- Furniture delivery mid February 2018

### Measure L – Phase 4 Projects


- Modernization Projects
  - Ruskin Elementary School FIS
    - Meeting with Site Staff to review design mid September 2017
    - Submit to DSA late October 2017
  - Piedmont Middle School FIS
    - Meeting with Site Staff to review design mid September 2017
    - Submit to DSA late October 2017
  - Brooktree Elementary School
    - Meeting with Site Staff to review design mid September 2017
    - Submit to DSA late October 2017
  - Cherrywood Elementary School
    - Meeting with Site Staff to review design mid September 2017
    - Submit to DSA late October 2017
  - Toyon Elementary School
    - Meeting with Site Staff to review design late September 2017
    - Submit to DSA late October 2017
  - Morrill Middle School
    - Meeting with Site Staff to review design mid September 2017
    - Submit to DSA late October 2017
  - AV @ MPR Elementary Schools
    - Order equipment September 2017
    - Install electrical requirement October 2017
    - Install AV equipment November 2017

## Measure L – Program Schedule

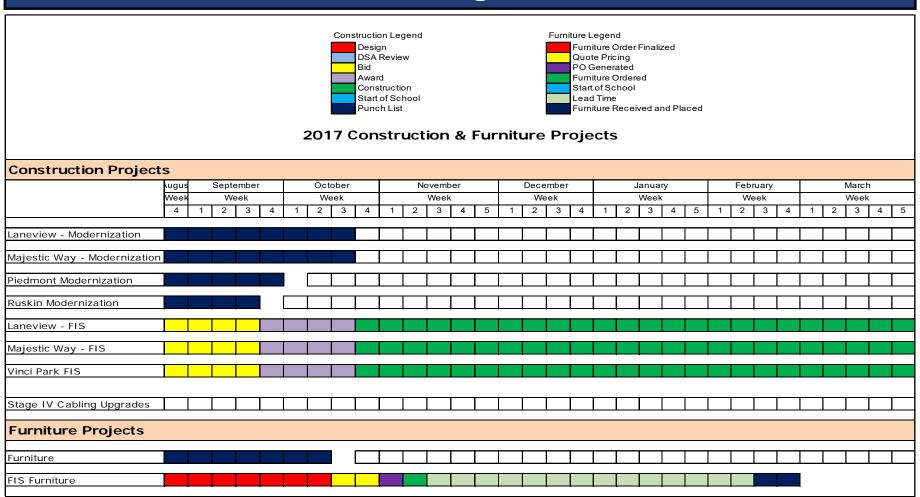

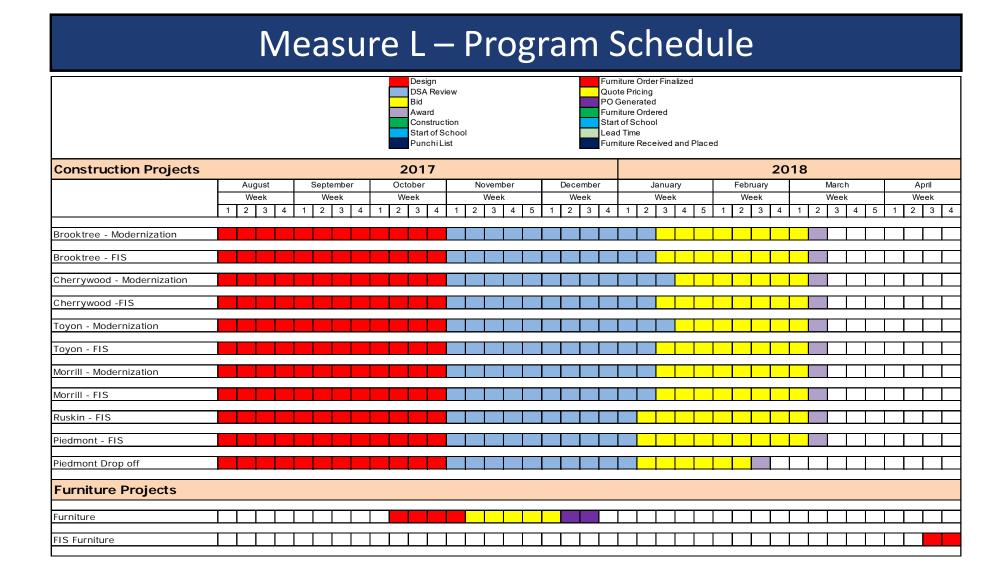

## Measure L – Program Schedule

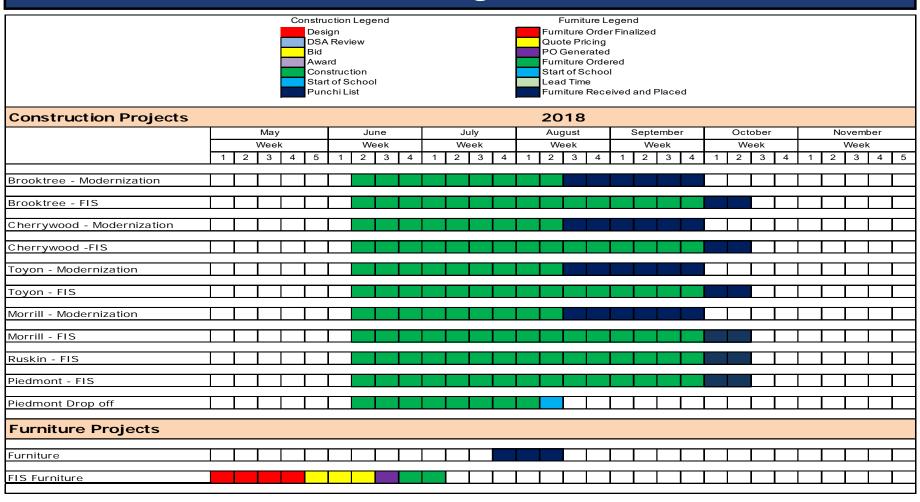



Thank You
