



MEASURE L BOND UPDATE

May 22, 2018

Measure L – Overview

- Phase 2 Project Update
- Phase 3 Project Update
- Phase 4 Project Update
- FIS and Classroom Furniture Update
- Program Schedule Review

Measure L – Phase 2 Projects

- Vinci Park Elementary School FIS
 - Phase 1 Interior Work
 - Ceiling replacement week of May 14, 2018
 - Phase 2 Exterior Work
 - DSA approval week of May 14, 2018

Measure L – Phase 2 Projects

Vinci Park FIS



Main FIS Space

Measure L – Phase 2 Projects

Vinci Park FIS



Main FIS Space

Measure L – Furniture

- FIS Furniture Vinci Park
 - Awaiting final quote from vendor
- FIS Furniture Laneview & Majestic Way
 - Delivery is complete
- Furniture 2018 Project
 - Meeting with Principal in May 2018
- Classroom Furniture 2018 Projects
 - Awaiting final quote from vendor

Measure L – Phase 4 Projects

- Ruskin Elementary School FIS
 - Notice of Award send to Construction on May 9, 2018
 - Start Construction June 11, 2018
- Piedmont Middle School FIS
 - Notice of Award send to Construction on May 9, 2018
 - Start Construction June 11, 2018
- Moving
 - Classroom/Library/Kitchen packing was completed on June 8, 2018
 - Waters Moving Company begin moving on June 8, 2017 @ 3:00 pm. Moving was completed by June 10, 2018
 - Administration staff is scheduled to be packed by June 26, 2018 and moved out by June 27, 2018


Measure L – Phase 4 Projects

- Brooktree Elementary School
 - FIS/Modernization Package
 - Notice of Award send to Construction on May 9, 2018
 - Start Construction June 11, 2018
 - Flooring Package
 - Start construction June 11, 2018
- Cherrywood Elementary School
 - Interior Painting Package
 - Notice of Award send to Construction on May 15, 2018
 - Start Construction June 11, 2018
 - Flooring Package
 - Start construction June 11, 2018
 - FIS/Modernization Package
 - A/E incorporating lift for second floor into drawings
 - A/E to set up DSA back check appointment for final approval
 - Start construction Fall 2018

Measure L – Phase 4 Projects

- Morrill Middle School
 - FIS/Modernization Package
 - Notice of Award send to Construction on May 9, 2018
 - Start Construction June 11, 2018
 - Flooring Package
 - Start construction June 11, 2018
- Toyon Elementary School
 - Interior/Exterior Painting Package
 - Notice of Award send to Construction on May 15, 2018
 - Start Construction June 11, 2018
 - Flooring Package
 - Start construction June 11, 2018
 - FIS/Modernization Package
 - Submit to DSA early May 2018
 - Construction to begin in Fall of 2018

Measure L – Program Schedule

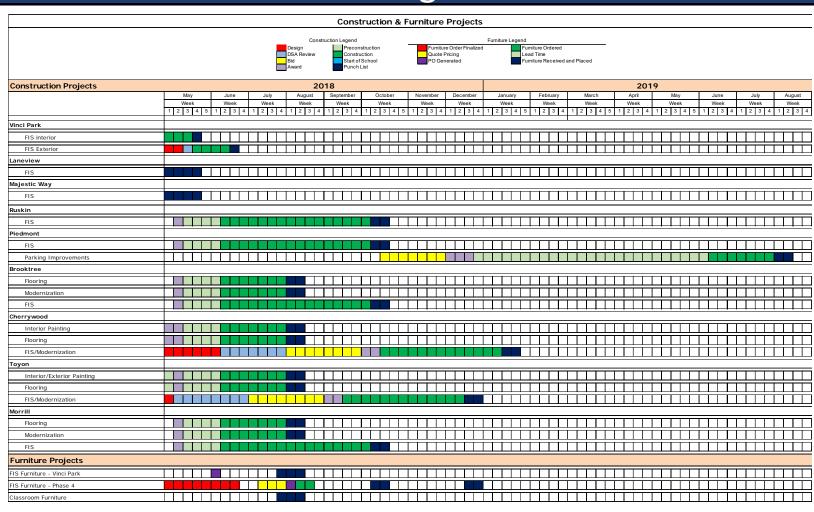



Thank You
