



# MEASURE L BOND UPDATE

June 19, 2018

## Measure L – Overview

- Project Updates
- FIS and Classroom Furniture Update
- Program Schedule Review

## Measure L – Project Updates

- Vinci Park Elementary School - FIS
  - Phase 1 – Interior Work
    - Complete
  - Phase 2 – Exterior Work
    - Work to start the week on 6/18
- Ruskin Elementary School - FIS
  - Beal's Martin and Associations started construction June 11, 2018
- Piedmont Middle School - FIS
  - Beal's Martin and Associations started construction June 11, 2018

## Measure L – Project Updates

- Moving
  - Classroom/Library/Kitchen packing was completed on June 8, 2018
  - Waters Moving Company begin moving on June 8, 2017 @ 3:00 pm. Moving was completed by June 10, 2018
  - Administration staff is scheduled to be packed by June 26, 2018 and moved out by June 27, 2018
- Brooktree Elementary School
  - FIS/Modernization Package
    - CRW Construction started construction June 11, 2018
  - Flooring Package
    - H.L. Murphy Start will start construction June 27, 2018

## Measure L – Project Updates

- Cherrywood Elementary School
  - Interior Painting Package
    - Tiber Painting will start construction June 26, 2018
  - Flooring Package
    - H.L. Murphy Start will start construction June 25, 2018
  - FIS/Modernization Package
    - DSA is currently reviewing for access to 2<sup>nd</sup> floor (FIS)
    - Start construction Fall 2018

## Measure L – Project Updates


- Toyon Elementary School
  - Interior/Exterior Painting Package
    - Color Chart Painting started construction June 11, 2018
  - Flooring Package
    - H.L Murphy started construction June 11, 2018
  - FIS/Modernization Package
    - Submit to DSA July 2018
    - Construction to begin in Fall of 2018
- Morrill Middle School
  - FIS/Modernization Package
    - Cal State Construction started construction June 11, 2018
  - Flooring Package
    - H.L Murphy started construction June 11, 2018

## Measure L – Project Updates



Cherrywood - MPR

## Measure L – Project Updates

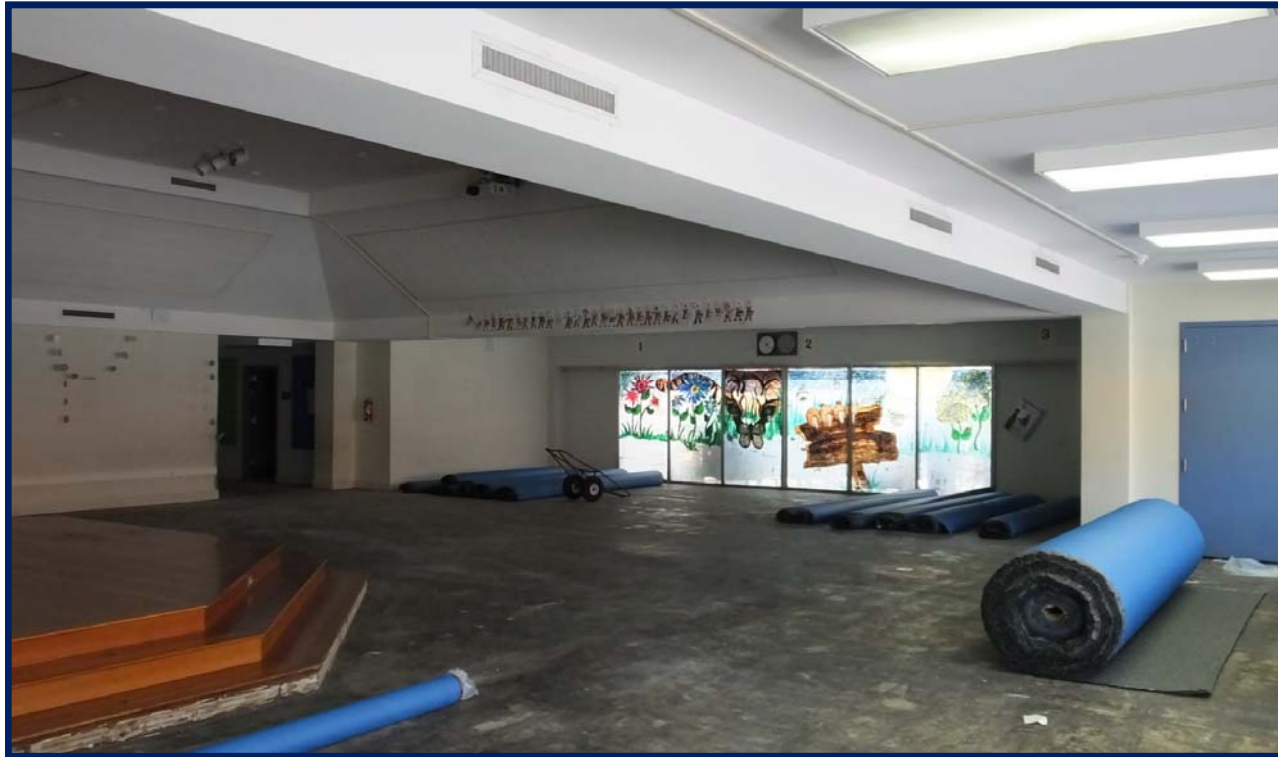

Toyon - MPR



## Measure L – Project Updates



Toyon – Kindergarten Classroom

## Measure L – Project Updates



Ruskin - FIS

## Measure L - Furniture

- FIS Furniture - 2018 Project
  - FIS furniture selection meetings to begin in June 2018
- Classroom Furniture - 2018 Projects
  - Classroom furniture has been ordered
  - Delivery scheduled starting the week on 7/23/18

# Measure L – Program Schedule

		2019																																																															
		June				July				August				September				October				November				December				January				February				March				April				May				June				July				August							
		Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week															
		1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
<b>Construction Projects</b>																																																																	
<b>Vinci Park</b>																																																																	
	FIS Exterior																																																																
<b>Ruskin</b>																																																																	
	FIS																																																																
<b>Piedmont</b>																																																																	
	FIS																																																																
	Parking Improvements																																																																
<b>Brooktree</b>																																																																	
	Flooring																																																																
	Modernization																																																																
	FIS																																																																
<b>Cherrywood</b>																																																																	
	Interior Painting																																																																
	Flooring																																																																
	FIS/Modernization																																																																
<b>Toyon</b>																																																																	
	Interior/Exterior Painting																																																																
	Flooring																																																																
	FIS/Modernization																																																																
<b>Morrill</b>																																																																	
	Flooring																																																																
	Modernization																																																																
	FIS																																																																
<b>Furniture Projects</b>																																																																	
	FIS Furniture - Phase 4																																																																
	Classroom Furniture																																																																

Construction Legend				Furniture Legend			
	Design		Preconstruction		Furniture Order Finalized		Furniture Ordered
	DSA Review		Construction		Quote Pricing		Lead Time
	Bid		Start of School		PO Generated		Furniture Received and Placed
	Award		Punch List				

# Northwood Elementary School Flexible Instructional Space

Thank You

