

The image shows the exterior of a building with a covered walkway. The walkway is supported by several thick, orange square pillars. Underneath the walkway, there are blue metal benches. The building has a white upper half and a grey lower half. A bright blue door is visible on the right side of the building. There are windows with white frames. A sign above the door says "TO OFFICE". The text "MEASURE L BOND UPDATE" is overlaid in the center of the image.

# MEASURE L BOND UPDATE

August 14, 2018

## Measure L – Overview

- Project Updates
- FIS and Classroom Furniture Update
- Program Schedule Review
- Presentation
  - Toyon FIS

## Measure L – Project Updates

- **Vinci Park Elementary School - FIS**
  - Phase 1 – Interior Work - Complete
  - Phase 2 – Exterior Work
    - Work to be completed by 8/17, with exception of FIS fencing
- **Ruskin Elementary School - FIS**
  - On schedule to complete in October 2018
- **Piedmont Middle School - FIS**
  - On schedule to complete in October 2018

## Measure L – Project Updates

- **Brooktree Elementary School**

- Modernization Project

- Provide path of travel to exterior student restrooms at playground - Complete
- ADA upgrades to exterior student restrooms - Complete
- ADA drinking fountain replacement - Complete
- ADA upgrades to staff restrooms - Complete
- Exterior glazing - Complete
- Interior painting - Complete

- Flooring Project

- Flooring - Complete

- Flexible Instruction Space is on schedule

## Measure L – Project Updates

- **Cherrywood Elementary School**
  - Interior Painting Project
    - Interior painting - Complete
  - Flooring Project
    - Flooring – Complete
  - Miscellaneous Work
    - Removal of casework at MPR - Complete
    - Install tackable wall panels at MPR – Complete
    - Classroom whiteboards - Complete
  - FIS
    - Submitted to DSA September 2018

## Measure L – Project Updates

- **Toyon Elementary School**

- Interior/Exterior Painting Project

- Interior painting - Complete
- Exterior painting - Complete

- Flooring Project

- Flooring - Complete

- Miscellaneous Work

- Exterior door replacement - Complete
- Stage partition repair - Complete
- Sink repair at classroom 1 - Complete
- Tinting/Painting of Classroom windows – anticipated completion Mid-September

## Measure L – Project Updates

- **Toyon Elementary School - continue**

- FIS

- Submitted to DSA 8/6
- Receive bids 10/30
- Recommendation of award at the November 13, 2018 meeting
- Start construction November 2018
- Completion February 2019

## Measure L – Project Updates

- **Morrill Middle School**

- Modernization Project


- Site concrete replacement at Administration entrance - Complete
- Site concrete replacement at northwest stairs - Complete
- Site concrete replacement between B & C - Complete
- Provide path of travel; ramp to blacktop area - Complete
- Upgrade to ADA parking – Complete
- Minor ADA upgrades to student restrooms – Complete
- ADA upgrades to staff restrooms – Complete
- Concrete slab repair at buildings B, C, D and E - Complete
- Interior painting – Complete
- Reconfigure of Library space – Complete
- Fencing – Chain link fencing is complete/ornamental fencing to be complete by 8/25



## Measure L – Project Updates


- **Morrill Middle School - continue**
  - Flooring Project
    - Flooring - Complete
  - Flexible Instruction Space is on schedule for completion in October
- **Moving**
  - Administration spaces moves in - Complete
  - Library/Kitchen moves will be completed by 8/8
  - Classrooms moves will be completed by 8/8

## Measure L – Project Updates

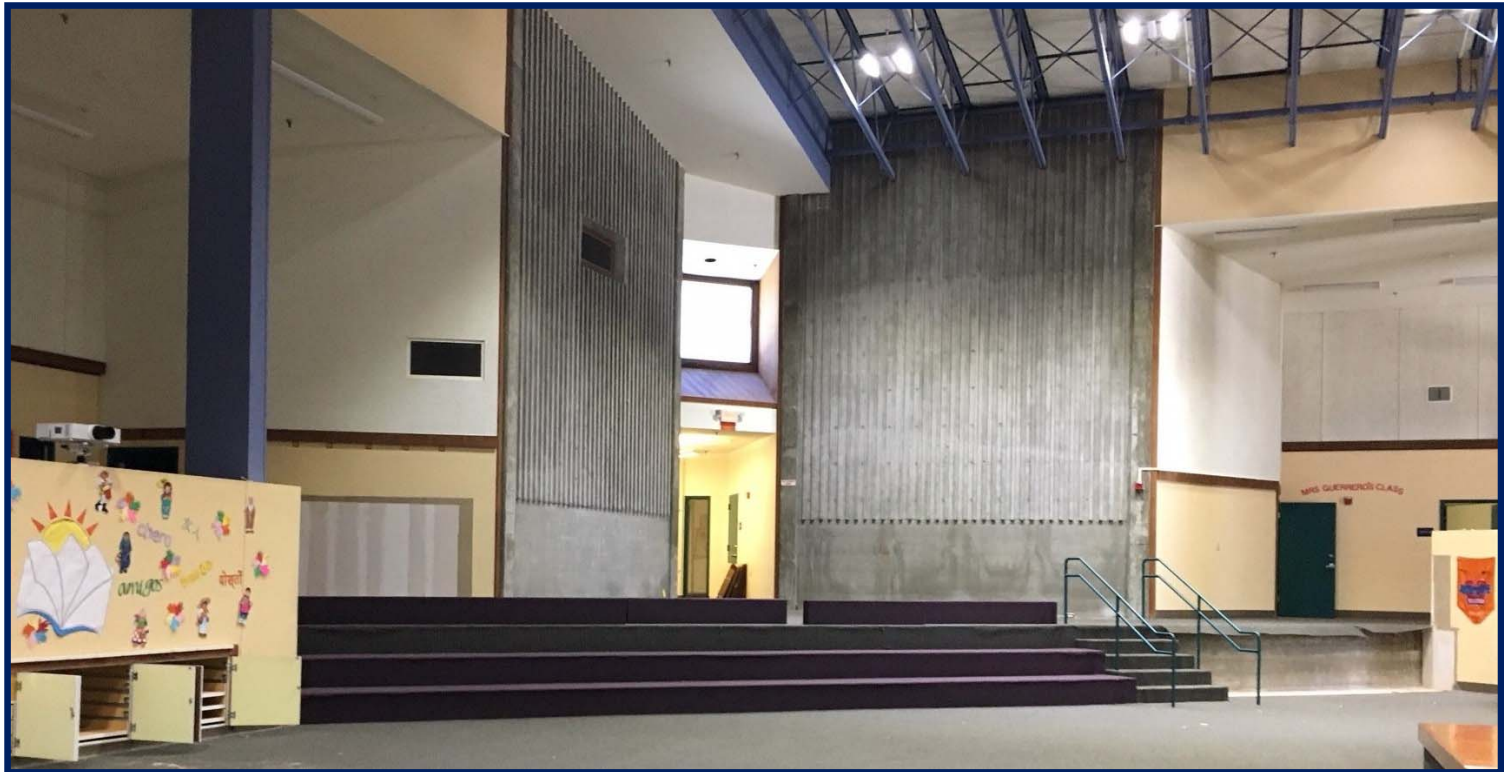

Cherrywood - MPR - Before

## Measure L – Project Updates

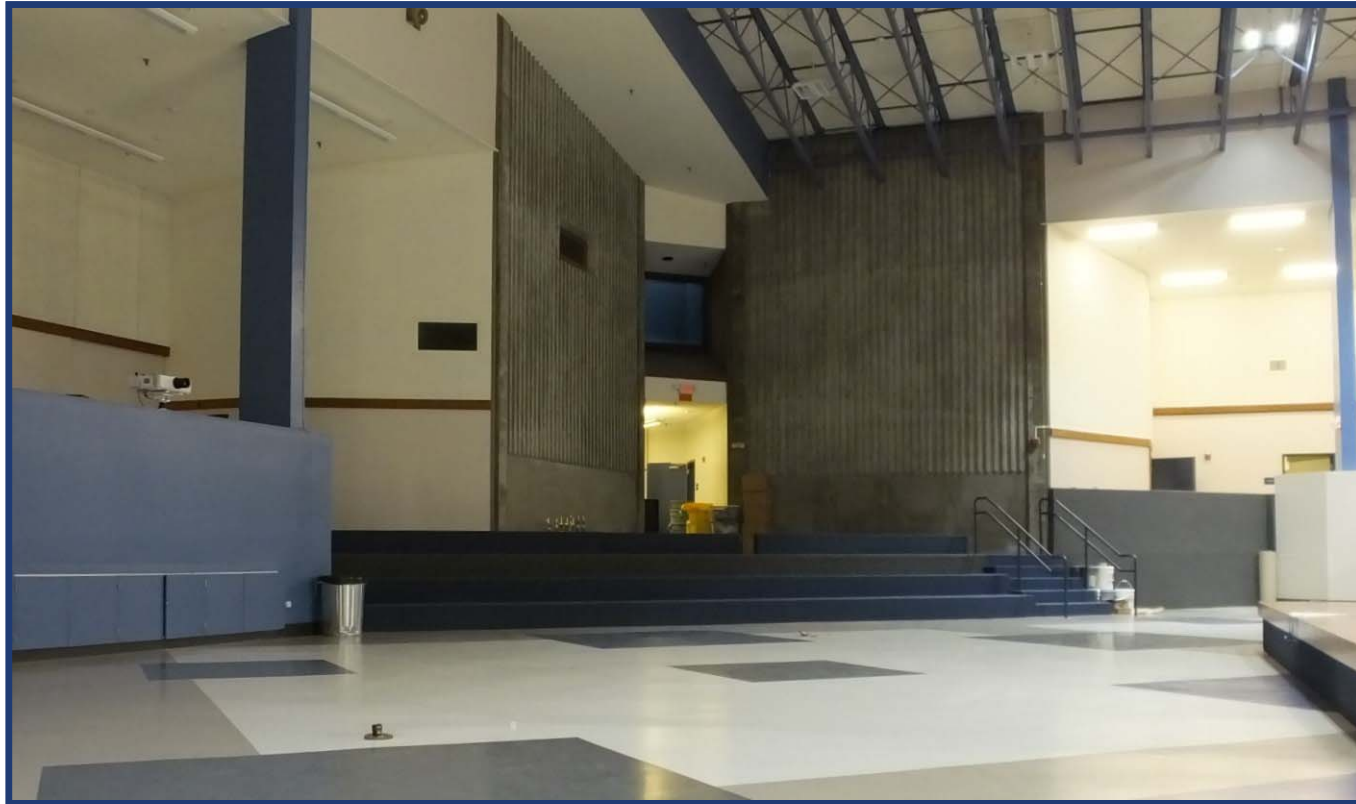

Cherrywood - MPR - After

## Measure L – Project Updates



Toyon - Exterior - Before



## Measure L – Project Updates



Toyon - Exterior - After

## Measure L – Project Updates



Toyon - Kindergarten Classroom - Before

## Measure L – Project Updates



Toyon - Kindergarten Classroom - After


## Measure L – Project Updates



Brooktree - MPR



## Measure L – Project Updates

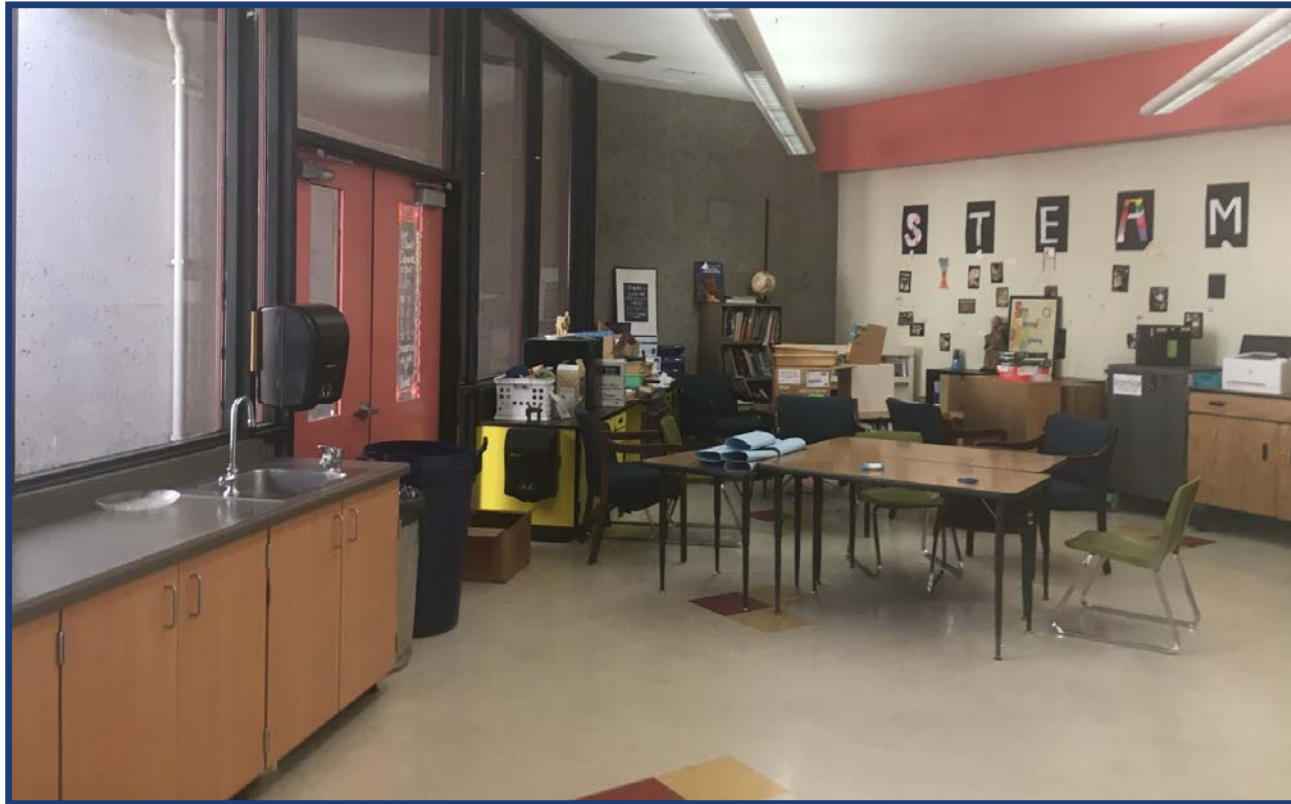

Brooktree - Work Room - Before

## Measure L – Project Updates



Brooktree - Work Room - After

## Measure L – Project Updates



Morrill - Main Entry - Before

## Measure L – Project Updates



Morrill - Main Entry - After



## Measure L – Project Updates



Morrill - Administration

## Measure L - Furniture

- **Classroom Furniture - 2018 Projects**
  - Classroom furniture delivery - Complete
- **FIS Furniture - 2018 Projects**
  - Meeting with principals

# Measure L – Program Schedule

Construction & Furniture Projects																																																											
2018																2019																																											
July				August				September				October				November				December				January				February				March				April				May				June				July				August							
Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week				Week											
1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
<b>Vinci Park</b>																																																											
FIS Exterior																																																											
Ruskin																																																											
FIS																																																											
Piedmont																																																											
FIS																																																											
Parking Improvements																																																											
Brooktree																																																											
Flooring																																																											
Modernization																																																											
FIS																																																											
Cherrywood																																																											
Interior Painting																																																											
Flooring																																																											
FIS/Modernization																																																											
Toyon																																																											
Interior/Exterior Painting																																																											
Flooring																																																											
FIS/Modernization																																																											
Morrill																																																											
Flooring																																																											
Modernization																																																											
FIS																																																											
<b>Furniture Projects</b>																																																											
FIS Furniture - Phase 4																																																											
Classroom Furniture																																																											

**Construction Legend**

- Design
- DSA Review
- Bid
- Award
- Preconstruction
- Construction
- Start of School
- Punch List


**Furniture Legend**

- Furniture Desing
- Quote Pricing
- PO Generated
- Furniture Ordered
- Lead Time
- Furniture Received and Placed

# Presentations

- Toyon – Flexible Instructional Space (FIS)





# Toyon Elementary School

Flexible Instruction Space

August 14, 2018

# Team Introductions

- **BUSD**

- Tony Kanastab – Director, Facilities and Modernization

- **Kitchell – Project Management**

- Jim Wilson – Project Director

- **McKim Design Group – Architect**

- Kirk McKim, Principal Architect
- Todd Walter, Director/Architect




# Toyon ES Flexible Instruction Space

- 1) Brief Overview of Scope
- 2) Q&A

# Scope Overview

- Flexible Instruction Complex
  - Convert existing Library space to Flexible Instruction Space
  - Convert adjacent Offices to Maker Space
  - Convert adjacent Offices & Workroom to Library/Bookroom
  - Convert adjacent Janitor/Junk outdoor exit space to Outdoor Learning Space.
- Restroom Modifications
  - For accessibility only
- Parking & Path-of-Travel upgrades for accessibility
- Entry concrete and walkway upgrades/replacement for accessibility & drainage
- Fencing adjacent to street access

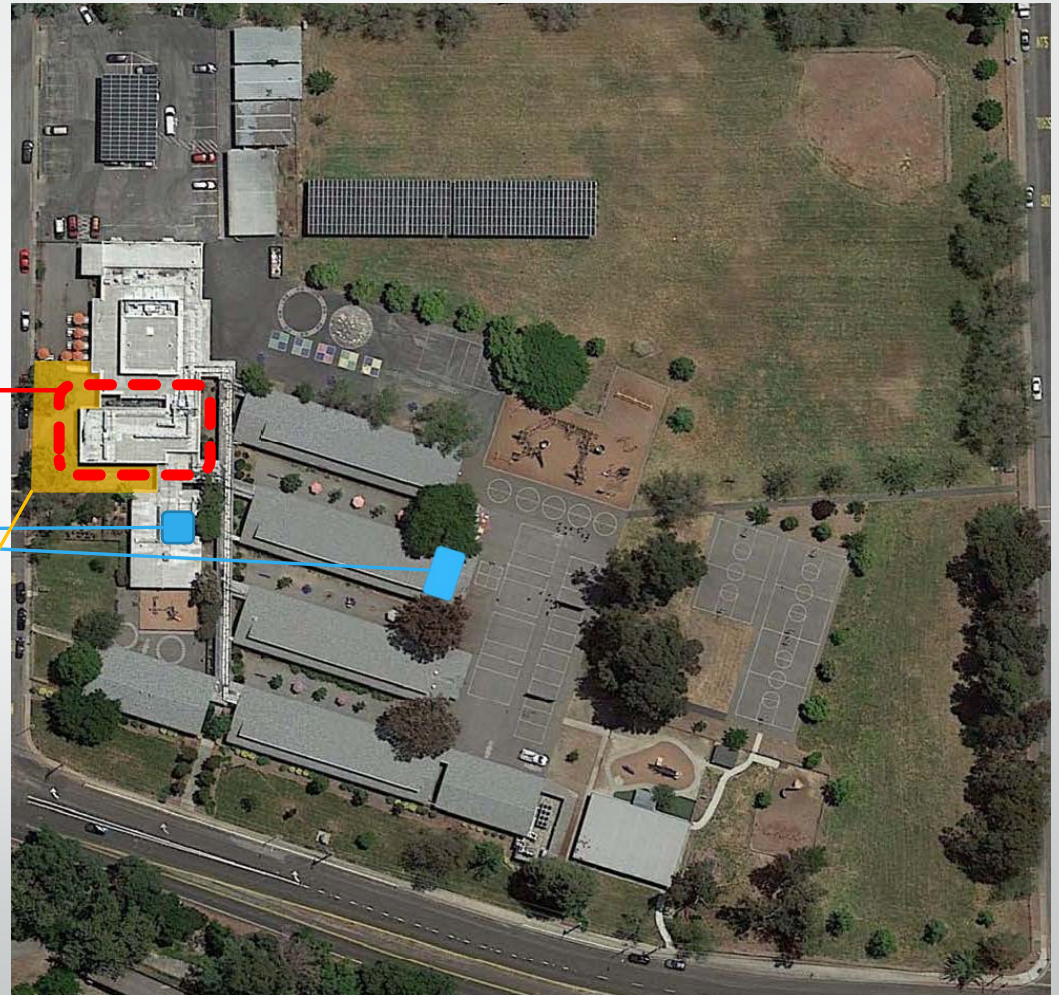

# Flexible Instructional Space – INDUSTRIAL

## OUTDOOR LAB

Outdoor Creation Space (Messy)

## MAKER SPACE


Design –  
Manufacture –  
Create

Display

Design- Collaborate - Assemble  
FLEXIBLE INSTRUCTION SPACE

## LIBRARY- BOOK ROOM

Investigate-  
Research

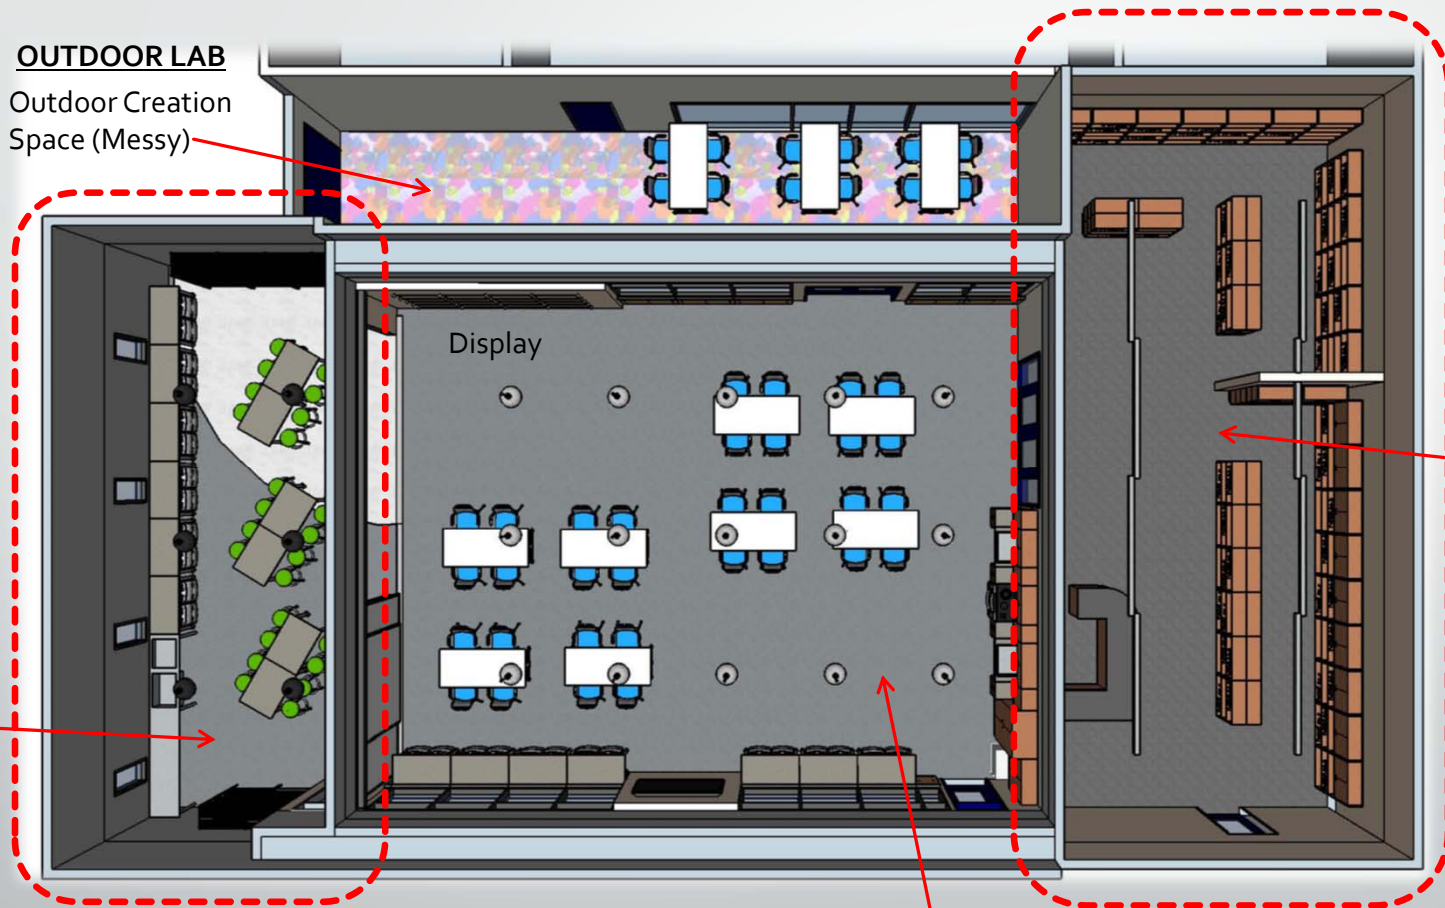



# Flexible Instructional Complex



Flexible Instructional Complex





## Flexible Instructional Complex





Library – Book Room



# Maker Space



# Maker Space






## Flexible Instruction Space



## Flexible Instruction Space

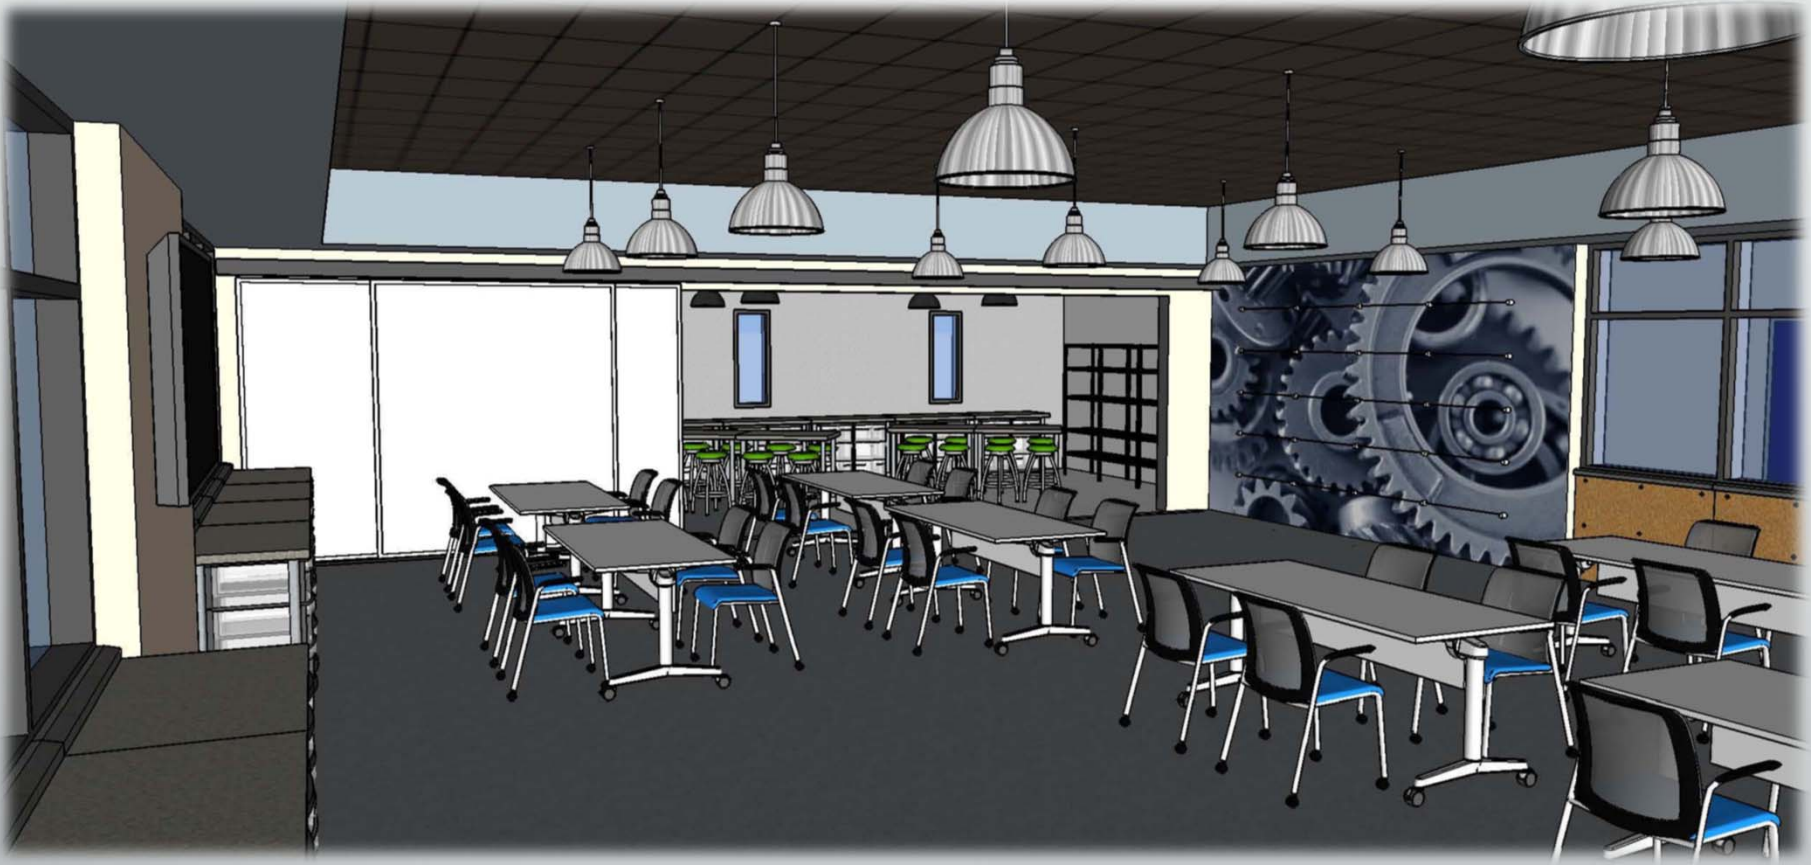

## Flexible Instructional Space





## Flexible Instruction Space



## Flexible Instruction Space





# Outdoor Lab





# Q&A



Thank You
