MEASURE L BOND UPDATE August 11, 2020

IIIÀ

Measure L – Overview

- Project Updates
- Program Schedule Review

- Complete
 - Cherrywood Window Graphic
 - Paving Laneview/Ruskin/Morrill
 - Library Shelving Brooktree, Majestic Way, Ruskin, and Vinci Park
- In progress:
 - Morrill HVAC
 - HVAC unit is scheduled for the week of August 10,2020
 - Scheduled to be completed on September 9, 2020
 - Flooring replacement at Building D (Science) Rooms 4,5,6, and 7
 - Paving for Lunch Shade Structure at Noble
 - Hydration Stations in the Cafeteria at Brooktree, Laneview, Majestic Way, Northwood, Summerdale, and Toyon
 - Replacement of HVAC Unit at District Office

- Bids Received
 - Perimeter Fencing Chain Link
 - Noble
 - Laneview
 - Toyon
 - Sierramont
 - Perimeter Fencing Ornamental
 - Ruskin
 - Noble FIS Mural
 - Lunch Shade Structures
 - Noble
 - Toyon
 - Covered Walkway at Toyon

- Bidding/Procurement:
 - Perimeter Fencing Ornamental
 - Sierramont
 - Toyon
 - Vinci Park FIS Canopy
 - Music Room Risers/Misc.
- Design:
 - Lunch Shade Structures
 - Morrill
 - Vinci Park
 - Piedmont
 - Entry Canopy
 - Marquee
 - Lunch Shade Structure

- Design:
 - Main Alarm Security Alarm Panels
 - Security Camera @ Middle Schools
 - Paving Projects
 - Brooktree
 - Northwood
 - Toyon
- Studies
 - HVAC Toyon
 - HVAC Brooktree, Majestic Way, and Summerdale



New Library Shelving




Laneview Staff Parking Lot




Morrill – Music Room HVAC Upgrade



Morrill – Music Room HVAC Upgrade

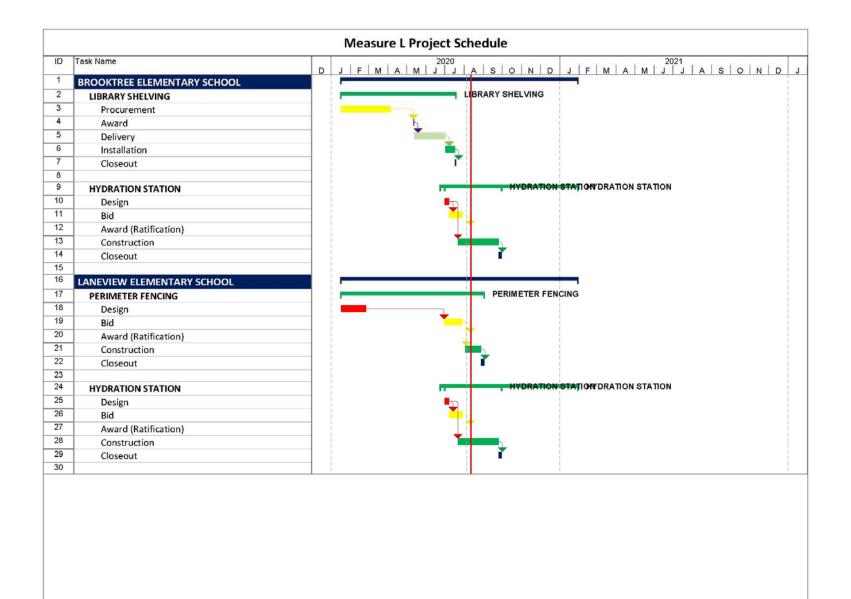

ID	Task Name	Measure L Project Schedule
31	MAJESTIC WAY ELEMENTARY SCHOOL	D J F M A M J J A S O N D J F M A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J A S O N D J F M A M J J A S O N D J A S O N D J J
32	LIBRARY SHELVING	LIBRARY SHELVING
33	Procurement	
34	Award	
35	Delivery	
36	Installation	
37	Closeout	
38	Closedut	
39	HYDRATION STATION	HYDRATION STATION STATION
40	Design	
41	Bid	
42	Award (Ratification)	
43	Construction	
44	Closeout	
45		
46	NOBLE ELEMENTARY SCHOOL	
47	FIS MURAL	FIS MURAL
48	Award (Ratification)	Ь
49	Construction	
50	Closeout	- · · · · · · · · · · · · · · · · · · ·
51		
52	PERIMETER FENCING	PERIMETER FENCING
53	Design	
54	Bid	
55	Award (Ratification)	
56	Construction	
57	Closeout	Ť
58		
59	LUNCH SHADE STRUCTURE	LUNCH SHADE STRUCTURE
60	Design	
61	DSA Review	
62	Bid	
63	Award (Ratification)	J. J
64	Fabrication/Delivery	
65	Construction	
	Closeout	
66 67		

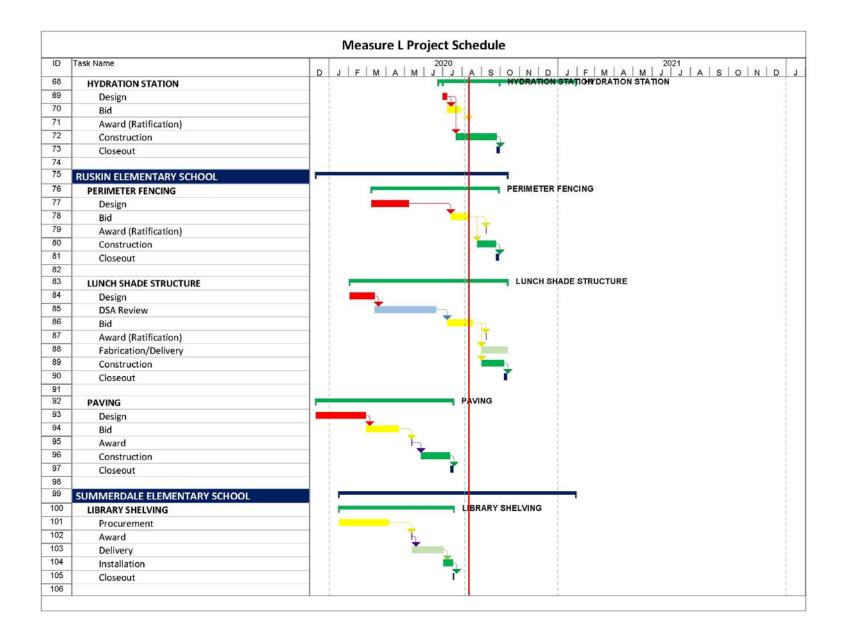

		Measure L Project Schedule
ID	Task Name	2020 2021 D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D HYDRATION STATION STATION
107	HYDRATION STATION	
108	Design	
109	Bid	X
110	Award (Ratification)	
111	Construction	Til
112	Closeout	Ť
113		
114	TOYON ELEMENTARY SCHOOL	
115	LUNCH SHADE STRUCTURE	LUNCH SHADE STRUCTURE
116	Design	
117	DSA Review	
118	Bid	
119	Award (Ratification)	
120	Fabrication/Delivery	
121	Construction	
122	Closeout	r
123		
124	COVERED WALKWAY STRUCTURE	COVERED WALKWAY STRUCTURE
125	Design	
126	DSA Review	
127	Bid	
128	Award (Ratification)	
129	Fabrication/Delivery	
130	Construction	
131	Closeout	
132 133		PERIMETER FENCING
133	PERIMETER FENCING	PERIMETER FENCING
134	Design Bid	
135		
137	Award (Ratification) Construction	
138		
139	Closeout	
140	HYDRATION STATION	HYDRATION STATION STATION
141	Design	
142	Bid	
143	Award (Ratification)	
144	Construction	
145	Closeout	

	Measure L Project Schedule					
ID	Task Name	D J F M A M J J A S O N D J F M A M J J A S O N D .				
146	VINCI PARK ELEMENTARY SCHOOL					
147	FIS CANOPY	FIS CANOPY				
148	Procurement					
149	Award (Ratification)					
150	Construction					
151	Closeout					
152						
153	LIBRARY SHELVING	LIBRARY SHELVING				
154	Procurement					
155	Award	K				
156	Delivery					
157	Installation					
158	Closeout					
159						
160	LUNCH SHADE STRUCTURE	LUNCH SHADE STRUCTURE				
161	Design					
162	DSA Review					
163	Bid					
164	Award (Ratification)					
165	Fabrication/Delivery					
166	Construction					
167	Closeout					
168						
169	MORRILL MIDDLE SCHOOL					
170	HVAC - MUSIC ROOM	HVAC - MUSIC ROOM				
171	Design					
172	DSA Review					
173	Bid					
174	Award					
175	Construction					
176	Closeout					
177						
178	LUNCH SHADE STRUCTURE	LUNCH SHADE STRUCT				
179	Design					
180	DSA Review					
181	Bid					
182	Award	- F				
183	Fabrication/Delivery					
184	Construction					
185	Closeout					

	Measure L Project Schedule					
ID	Task Name	2020 D J F M A M J J A S O N D J F M A M J J A S O N D .				
186						
187	PIEDMONT MIDDLE SCHOOL	PIEDMONT MIDDLE SCH				
188	ENTRY CANOPY	ENTRY CANOPY				
189	Design					
190	DSA Review					
191	Bid					
192	Award					
193	Fabrication/Delivery					
194	Construction					
195	Closeout	Ť				
196						
197	MARQUEE	MARQUEE				
198	Design					
199	DSA Review					
200	Bid					
201	Award	<u> </u>				
202	Fabrication/Delivery					
203	Construction					
204	Closeout	ř				
205						
206	LUNCH SHADE STRUCTURE	LUNCH SHADE STRUCT				
207	Design					
208	DSA Review					
209	Bid					
210	Award					
211	Fabrication/Delivery					
212	Construction					
213	Closeout	r r				
214						
	SIERRAMONT MIDDLE SCHOOL					
216	PERIMETER FENCING - Phase 1	PERIMETER FENCING - Phase 1				
217	Design					
218	Bid					
219	Award (Ratification)					
220	Construction					
221	Closeout	Ĩ				
222						

