



MEASURE L BOND

CONSTRUCTION UPDATE

September 13, 2016


Introduction

The following presentation is intended to provide the Board of Trustees with an update on the progress of Measure L Construction Bond Projects. These are projects that are currently active throughout the District.




Measure L – 2016 Project Overview

1. Phase 2 Technology Upgrade –Cable
2. Central Kitchen
3. F.I.S./Modernization/Classroom Furniture
 - Noble
 - Northwood
 - Sierramont Middle
 - Summerdale
 - Vinci Park [no F.I.S.]
4. Paving Projects
 - Morrill, Noble, Sierramont, Vinci Park
5. Energy Conservation – Solar

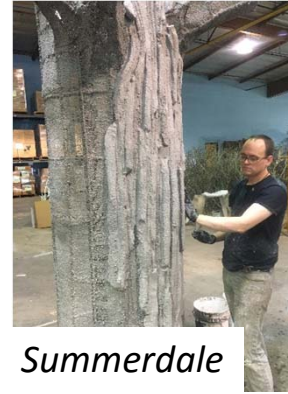

Summerdale

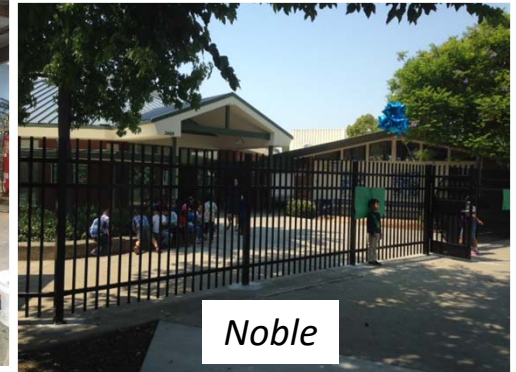

Noble



Morrill

Measure L – 2016 Project Details

1. Phase II Technology Upgrade - Cabling

a. Stage I Cabling Upgrades:



- Majestic Way, Piedmont, Toyon, Summerdale – completed
- Laneview:
 - ✓ Buildings A & C – completed
 - ✓ Buildings B, D & portables to be completed Feb. & Apr. 2017 breaks
- FIS Cabling & Exterior Wireless Access Points – in progress

b. Stage II Cabling Upgrades –

- MOT awarded – Thanksgiving Break

c. Stage III Cabling Upgrades:

- Noble awarded – Winter Break

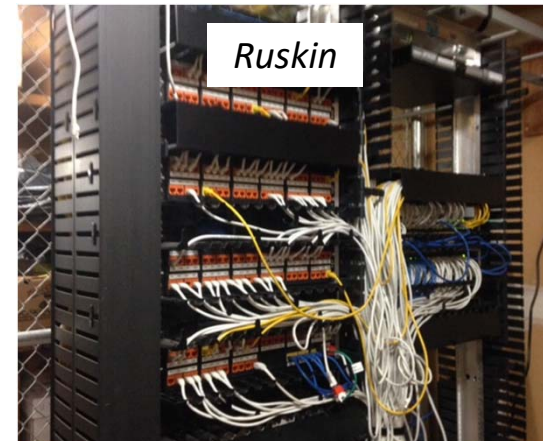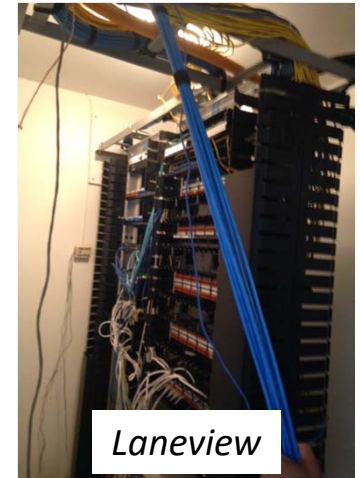

Measure L – 2016 Project Details

1. Central Kitchen

- Bid – 9/22/16
- Award – 10/18/16

2. F.I.S./Modernization Projects:

- Northwood:
 - Façade 9/17/16
 - Specialty doors & Walls: 11/15/16
 - Ceiling and lighting: 10/7/16
- Summerdale:
 - Ceiling and lighting: 9/27/16
- Noble:
 - Shade structure: 10/8/16
 - Specialty doors : 11/21/16
- Sierramont:
 - Specialty walls: 9/24/16
- Stage curtains: Noble, Northwood, Summerdale, Vinci
- F.I.S. furniture – order placed – Aug. 29, 2016 – 4-6 week lead time expected



Northwood F.I.S




Sierramont

Measure L – 2016 Project Details

3. Paving Projects

- Majority of work is completed
 - Sierramont east access – Sept 2016

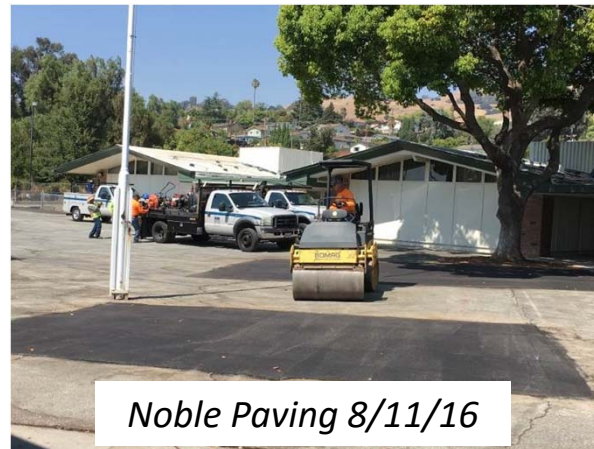

Measure L – 2016 Project Details



4. Solar Installation:

- Arrays wired at 12 of 13 sites
 - Remaining site: Piedmont
- All arrays to be completed by Sept. 9, 2016
- Electrical connection to PG&E – not finalized
 - Tentative start - Sept. 20, 2016
 - Tentative completion - Oct. 2, 2016



Measure L – 2017 Project Overview

1. Stage IV Cabling Upgrades
 - Brooktree, Northwood, Ruskin, Vinci Park - awarded
2. Central Kitchen
 - Tentative completion – April 2017
3. F.I.S./Modernization/Classroom Furniture
 - Laneview, Majestic Way
 - Vinci Park (F.I.S. only)
4. Modernization/Classroom Furniture
 - Piedmont, Ruskin
5. Pavement Rehabilitation
 - Brooktree, Cherrywood, Majestic Way
 - Piedmont Drop-Off Area

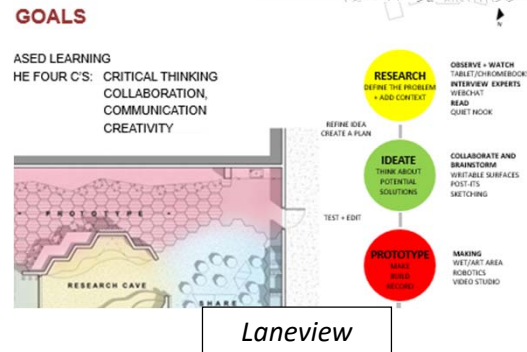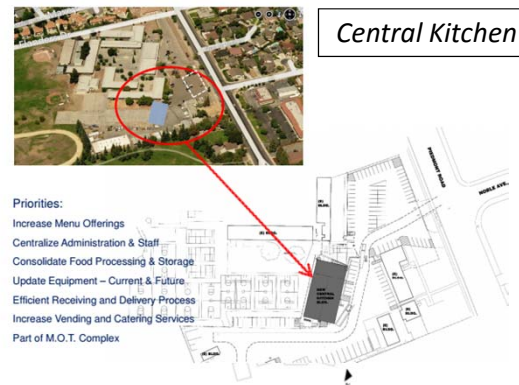

2016 Construction & Furniture Projects

Construction Legend	Furniture Legend
■ Design	■ Furniture Order Finalized
■ Bid	■ Quote Date
■ Award	■ Award
■ Construction	■ Furniture Ordered
■ Start of School	■ Start of School
■ Long Lead Items	■ Lead Time
■ Project Complete	■ Furniture Received and Placed

2016 Construction Projects

	August Week					September Week				October Week				November Week					December Week				January Week			
	1	2	3	4	5	1	2	3	4	1	2	3	4	1	2	3	4	5	1	2	3	4	1	2	3	4
Central Kitchen Const & Equip																										
Sierramont Chiller Upgrade																										
Sierramont FIS/Modernization																										
Noble FIS/Modernization																										
Northwood FIS/Modernization																										
Summerdale FIS/Modernization																										
Vinci Park/Modernization																										
Paving Rehabilitation																										
Solar Project																										
Stage I Cabling Upgrades																										
Stage II Cabling Upgrades																										
Stage III Cabling Upgrades																										

2016 Furniture Projects

Furniture																										
FIS Furniture																										

2017 Construction & Furniture Projects

Construction Legend

	Design
	Bid
	Award
	Construction
	Start of School
	Long Lead Items
	Project Complete

Furniture Legend

	Furniture Order Finalized
	Quote Date
	Award
	Furniture Ordered
	Start of School
	Lead Time
	Furniture Received and Placed

2017 Construction Projects

	August					September				October				November					December				January			
	Week					Week				Week				Week					Week				Week			
	1	2	3	4	5	1	2	3	4	1	2	3	4	1	2	3	4	5	1	2	3	4	1	2	3	4
Laneview FIS/Modernization																										
Majestic Way FIS/Modernization																										
Vinci Park FIS																										
Piedmont/Modernization																										
Ruskin/Modernization																										
Paving Rehabilitation																										
Piedmont Dropoff																										
Stage IV Cabling Upgrades																										

2017 Furniture Projects

Furniture																										
FIS Furniture																										



Please Join Us at the Ribbon Cutting Event – Thursday
10/13/16, 2:00 p.m. at a site to be determined

Thank You
