



MEASURE L BOND

CONSTRUCTION UPDATE

February 28, 2017

Introduction

The following presentation is intended to provide the Board of Trustees with an update on the progress of Measure L Construction Bond Projects. These are projects that are currently active throughout the District.



Noble FIS



Summerdale FIS

Measure L – 2016 Project Overview

- Phase 2 Technology Upgrade – Cable
- Remaining Work by School
- Energy Conservation – Solar
- Central Kitchen – On Schedule



Measure L – 2016 Project Details

➤ Phase II Technology Upgrade - Cabling

a. Stage I Cabling Upgrades:


- FIS Cabling – completed
- Exterior Wireless Access Points:
 - Majestic Way, Noble, Northwood, Piedmont, Summerdale, Toyon - completed
- Laneview:
 - ✓ Buildings B, D & portables to be completed April 2017 breaks

b. Stage II Cabling Upgrades:

- MOT awarded – Completed

c. Stage III Cabling Upgrades:

- Noble awarded – Completed

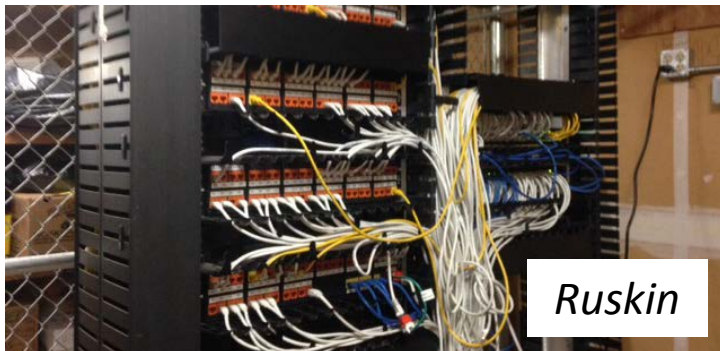

Measure L – Remaining Work by School

1. Noble ES:

- FIS Furniture – **Completed**
- Specialty doors : **3/31/17**
- FIS AV & Electrical: *In progress*
- MPR AV & Electrical: *In progress*

2. Northwood ES:

- FIS Furniture: **Completed**
- FIS AV & Electrical: *In progress*
- MPR AV & Electrical: *In progress*

3. Sierramont MS:

- FIS Audio Visual & Electrical: *In progress*
- Gym AV & Electrical: *In progress*

4. Summerdale ES:


- Fence installation: **2/24/17**

5. Vinci Park ES:

- Fence installation: *In progress*



Noble - before

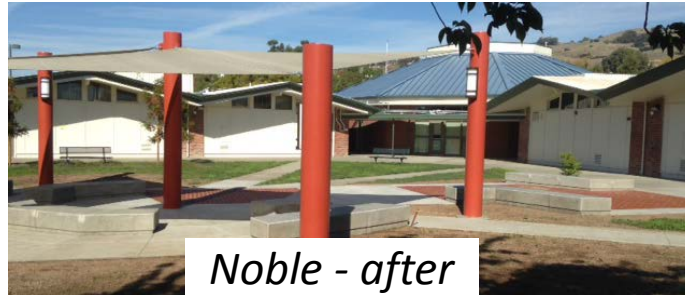

Noble - after

Measure L – Solar Project Update

- DSA closeout process has begun. The District has started to receive “Certification of Compliance Letters” from DSA.



Measure L – 2017 Project Overview

1. Stage IV Cabling Upgrades

- Brooktree, Northwood, Ruskin, Vinci Park – awarded – Summer 2017

2. Central Kitchen – expected completion

May 2017

3. Pavement Rehabilitation

- Brooktree, Cherrywood, Majestic Way
- Piedmont Drop-Off Area

4. March Project Presentations

- Laneview – FIS/Modernization
- Majestic Way – FIS/Modernization
- Piedmont – Modernization
- Ruskin – Modernization
- Vince Park - FIS



Central Kitchen

2016 Construction & Furniture Projects

Construction Legend

- Design
- Bid
- Award
- Construction
- Start of School
- Long Lead Items & Added Project Scope
- Project Complete

Furniture Legend

- Furniture Order Finalized
- Quote Pricing
- PO Generated
- Furniture Ordered
- Start of School
- Lead Time
- Furniture Received and Placed

2016 Construction Projects

	February				March					April				May					June							
	Week				Week					Week				Week					Week							
	1	2	3	4	1	2	3	4	5	1	2	3	4	1	2	3	4	5	1	2	3	4				
Central Kitchen Const & Equip																										
Sierramont FIS/Modernization																										
Noble FIS/Modernization																										
Northwood FIS/Modernization																										
Summerdale FIS/Modernization																										
Vinci Park Modernization																										
Paving Rehabilitation																										
Solar Project																										
Stage I Cabling Upgrades																										
Stage II Cabling Upgrades																										
Stage III Cabling Upgrades																										

2016 Furniture Projects

Furniture																										
FIS Furniture																										



Thank You
