



MEASURE L BOND UPDATE

February 27, 2018

Measure L – Overview

- Phase 2 Project Update
- Phase 3 Project Update
- Phase 4 Project Update
- FIS and Classroom Furniture Update
- Program Schedule Review

Measure L – Phase 2 Projects

- Vinci Park FIS Project (Phase 1)– Project is on schedule to be completed in March



Main FIS space

Measure L – Phase 2 Projects

- Pavement Rehabilitation – Piedmont Middle School
 - Project approved by DSA
 - Receive bids March 2018
 - Construction starts June 2018
- Vinci Park Elementary School - FIS
 - Phase 2 - Exterior Canopy and Site work
 - CGS (California Geological Survey) has approved the project
 - Meeting with DSA in early March for Canopy approval
 - Procurement/installation of exterior canopy and site related work completed by May 1, 2018

Measure L – Phase 3 Projects

Laneview FIS Project – Project to be completed by March 5, 2018



Main FIS space

Measure L – Phase 3 Projects

Laneview FIS Project



Small group space

Measure L – Phase 3 Projects

Laneview FIS Project



Fencing between and Main building and Kindergarten

Measure L – Phase 3 Projects

Majestic Way FIS Project – Project to be completed on March 12, 2018



Main FIS space

Measure L – Phase 3 Projects

Majestic Way FIS Project



FIS sink area


Measure L – Furniture

- FIS Furniture - Vinci Park
 - Awaiting final quote from vendor
 - Furniture delivery April 2018
- FIS Furniture - Laneview & Majestic Way
 - Furniture delivery on March 2, 2018
- FIS Furniture - 2018 Project
 - Meeting with Principal in March 2018
- Classroom Furniture - 2018 Projects
 - Submitting order to vendor for quote in February 2018

Measure L – Phase 4 Projects

- Modernization Projects
 - Ruskin Elementary School - FIS
 - Receive bids in March 2018
 - Piedmont Middle School - FIS
 - Receive bids in March 2018
 - Brooktree Elementary School
 - Receive bids in April 2018
 - Cherrywood Elementary School
 - Interior Painting Package -Receive bids March 2018
 - Mod/FIS Package – Awaiting structural comments from DSA
 - Meeting with DSA in March to review wheelchair lift option
 - Toyon Elementary School
 - Interior/Exterior Painting Package – Receive bids March 2018
 - FIS
 - Submit to DSA early May 2018
 - Construction to begin in Fall of 2018
 - Morrill Middle School
 - Receive bids in April 2018

Measure L – Program Schedule

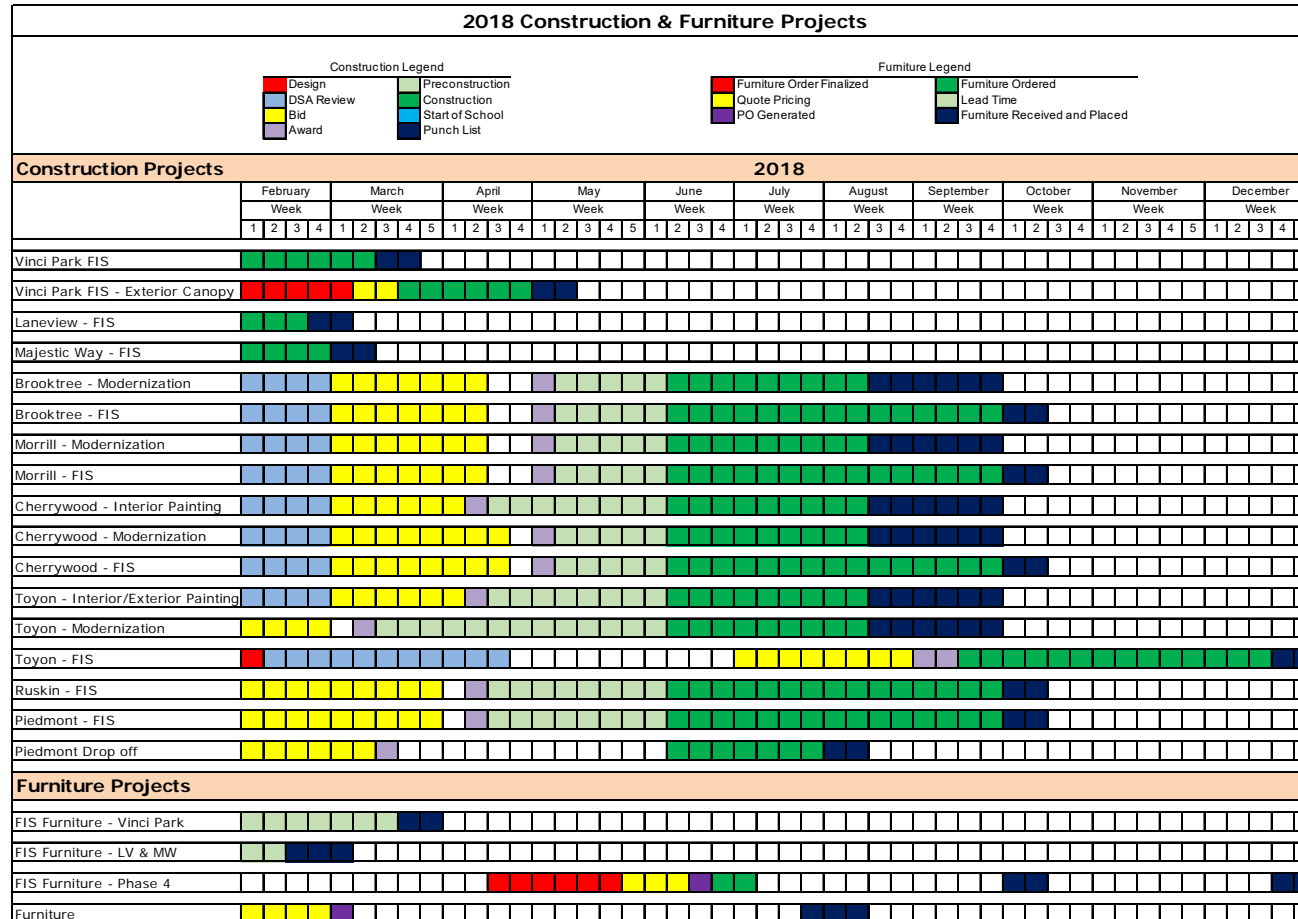



Thank You
