



MEASURE L BOND UPDATE

October 16, 2018

Measure L – Overview

- Project Updates
- Program Schedule Review

Measure L – Project Updates

- **Vinci Park Elementary School - FIS**
 - Phase 2 – Exterior Work
 - FIS fencing
 - Installation of exterior sink
- **Piedmont Middle School - FIS**
 - Fencing - gate replacement for ADA
 - Flexible Instruction Space is on schedule on schedule to complete in October
- **Piedmont Middle School - Parking**
 - Schedule to receive bids in December 2018/January 2019
 - Recommendation of award at the January 15, 2019 Board Meeting
 - Construction is scheduled to start June 2019

Measure L – Project Updates

- **Ruskin Elementary School - FIS**

- Replace existing fencing panels with decorative fence panels and fencing
- Flexible Instruction Space is scheduled to complete in late October/early November

- **Brooktree Elementary School - FIS**

- Flexible Instruction Space is scheduled to complete in late October/early November

- **Cherrywood Elementary School - FIS**

- Submitted to DSA with approval expected by early October
- Schedule to receive bids in early January 2019
- Recommendation of award at the January 15, 2019 Board Meeting
- Construction is scheduled to start April 2019

Measure L – Project Updates

- **Toyon Elementary School - FIS**

- Receive bids 10/30
- Recommendation of award at the November 13, 2018 meeting
- Start construction November/December 2018
- Completion FIS - February 2019 / Site Work – March 2019

- **Morrill Middle School**


- Completed Portion of the Modernization Project:
 - Fencing
- In Progress:
 - Flexible Instruction Space is scheduled for completion in late October/mid November

Measure L – Project Updates

- **Northwood Elementary School - Portable Relocation**

- The project was approved by DSA on September 27, 2018.
- The Construction Manager is presently procuring bids for the project
- The majority of the work will be completed during off hours or on the weekend.
- Work is anticipated to be completed by the end of October/early November

Measure L – Project Updates

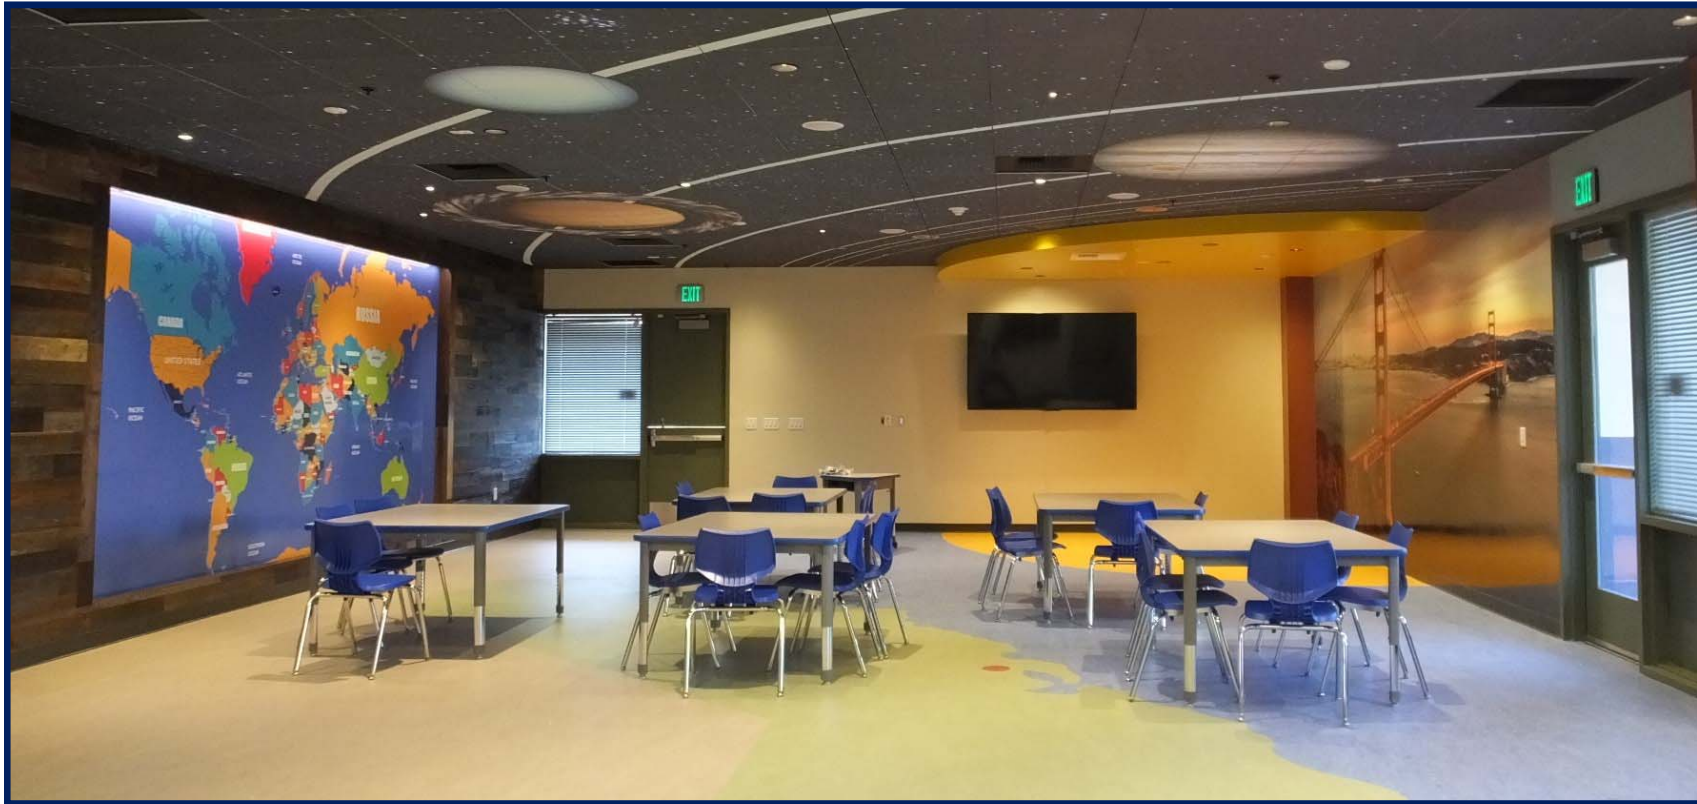

Vinci Park - FIS

Measure L – Project Updates



Ruskin - FIS

Measure L – Project Updates



Ruskin - FIS

Measure L – Project Updates



Piedmont - FIS

Measure L – Project Updates



Piedmont - FIS

Measure L – Project Updates



Brooktree – FIS

Measure L – Project Updates



Brooktree – FIS

Measure L – Project Updates



Morrill - FIS

Measure L – Project Updates



Morrill - FIS

Measure L – Project Updates



Morrill – Exterior Fencing

Measure L – Program Schedule

Construction & Furniture Projects																																			
<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;"> <p>Construction Legend</p> <ul style="list-style-type: none"> ■ Design ■ DSA Review ■ Bid ■ Award ■ Preconstruction ■ Construction ■ Start of School ■ Punch List </div> <div style="text-align: center;"> <p>Furniture Legend</p> <ul style="list-style-type: none"> ■ Furniture Desing ■ Quote Pricing ■ PO Generated ■ Furniture Ordered ■ Lead Time ■ Furniture Received and Placed </div> </div>																																			
Construction Projects	2018					2019																													
	October		November			December			January		February		March		April		May		June		July		August												
	Week		Week			Week			Week		Week		Week		Week		Week		Week		Week		Week												
	1	2	3	4	5	1	2	3	4	1	2	3	4	1	2	3	4	5	1	2	3	4	5	1	2	3	4	1	2	3	4	1	2	3	4
Vinci Park																																			
FIS Exterior																																			
Ruskin																																			
FIS																																			
Piedmont																																			
FIS																																			
Parking Improvements																																			
Brooktree																																			
FIS																																			
Cherrywood																																			
FIS/Modernization																																			
Toyon																																			
FIS																																			
FIS/Modernization - Site Work																																			
Morrill																																			
FIS																																			
Furniture Projects																																			
FIS Furniture - Phase 4																																			



Thank You
