

Measure L – Overview

- Project Updates
- Program Schedule Review

- Vinci Park Elementary School FIS
 - Phase 2 Exterior Work
 - Scheduled to complete in mid November
- Piedmont Middle School FIS
 - Flexible Instructional Space is scheduled to complete in mid November
- Piedmont Middle School Parking
 - Schedule to receive bids in December 2018
 - Recommendation of award at the January 15, 2019 Board Meeting
 - Construction is scheduled to start June 2019

- Ruskin Elementary School FIS
 - Flexible Instructional Space is scheduled to complete in mid November
- Brooktree Elementary School FIS
 - Flexible Instructional Space is scheduled to complete in mid November
- Cherrywood Elementary School FIS
 - DSA has approved the project
 - Project is currently out to bid, scheduled to receive bids in December
 - Recommendation of award at the January 15, 2019 Board Meeting
 - Construction is scheduled to start January 2019

Toyon Elementary School - FIS

- Receive bids October 31, received 7 bids and are within budget
- Recommendation of award at the November 13, 2018 meeting
- Start construction December 2018
- Completion FIS March 2019

Morrill Middle School

- In Progress:
 - Flexible Instructional Space is scheduled for completion in late November

- Northwood Elementary School Portable Relocation
 - DSA approval requires the District to add a driveway approach and vehicle gate at the southwest corner of the site
 - The Architect is working with the City of San Jose on the required permits
 - Work is anticipated to be completed by the end of November/early December




Ruskin - FIS



Piedmont - FIS



Piedmont - FIS

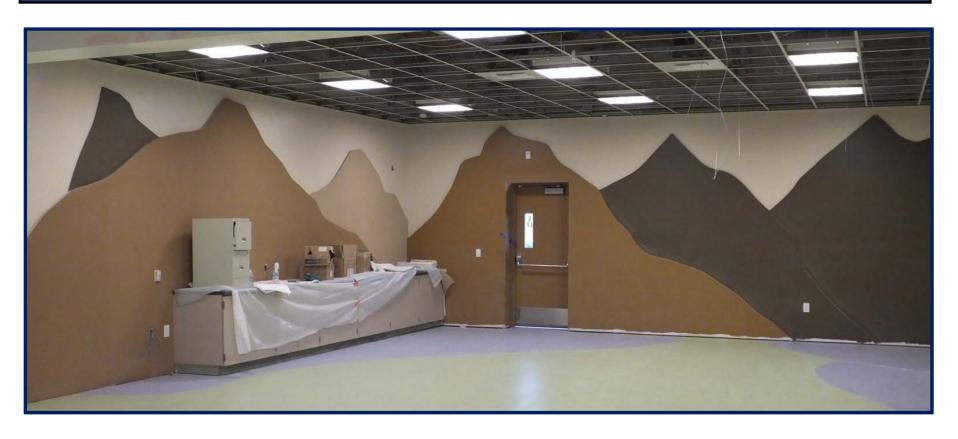

Brooktree – FIS



Brooktree – FIS



Morrill - FIS



Morrill - FIS

Measure L – Program Schedule

