

# MEASURE L BOND

CONSTRUCTION UPDATE

August 9, 2016

# Introduction

The following presentation is intended to provide the Board of Trustees with an update on the progress of Measure L Construction Bond Projects. These are projects that are currently active throughout the District.







## Measure L – 2016 Project Overview

- 1. Phase 2 Technology Upgrade Cable
- 2. Central Kitchen
- 3. F.I.S./Modernization/Classroom Furniture
  - Noble
  - Northwood
  - Sierramont Middle
  - Summerdale
  - Vinci Park [no F.I.S.]
- 4. Paving Projects
  - Morrill, Noble, Sierramont, Vinci Park
- 5. Energy Conservation Solar





- 1. Phase II Technology Upgrade Cabling
  - Stage I Cabling Upgrades:
    - Unforeseen work causing delays
    - Piedmont, Toyon, Summerdale near completion
    - Majestic Way in progress
    - Laneview potentially delayed, may complete individual wings during Feb. & Apr. 2017 breaks
  - Stage II Cabling Upgrades
    - MOT awarded Thanksgiving Break
  - Stage III Cabling Upgrades:
    - Noble awarded Winter Break



#### 1. Central Kitchen

- Bid Late August 2016
- Tentative award

  October 2016

#### 2. F.I.S./Modernization Projects

- Modernization & class furniture mostly on schedule
  - Delayed Items:
     Northwood Façade start of school
     Sierramont Chiller delayed Sept 2016
     Sierramont Library Circulation Desk Late Aug 2016
- F.I.S. delayed for long lead items
  - Specialty doors & walls: Noble, Sierramont
  - Ceiling treatments: Noble, Northwood, Summerdale
  - Noble Shade Structure
- F.I.S. furniture order placement pending



#### 3. Paving Projects

- Majority of work is complete
- Work areas remaining have heavy loads traveling on them. After that work is complete paving will be completed shortly thereafter:
  - Noble access to FIS Sept 2016
  - Sierramont east access Sept 2016



**Before** 




After

#### 4. Solar Installation:

- Arrays installed at 7 of 13 sites
  - Completed sites: Cherrywood, Morrill, Noble, Northwood, Sierramont, Summerdale, Vinci Park
- All arrays to be completed by Aug. 18, 2016
- Electrical connection to PG&E:
  - Starts Aug. 2016
  - Completion Oct. 2016



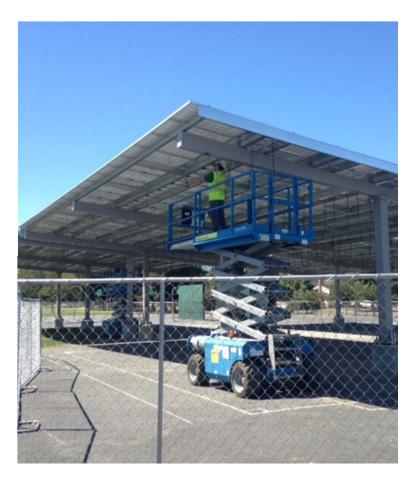

## Measure L – 2017 Project Overview

#### 1. Stage IV Cabling Upgrades

- Brooktree, Northwood, Ruskin, Vinci Park awarded
- 2. Central Kitchen
  - Tentative completion May 2017
- 3. F.I.S./Modernization/Classroom Furniture
  - Laneview, Majestic Way
  - Vinci Park (F.I.S. only)
- 4. Modernization/Classroom Furniture
  - Piedmont, Ruskin
- 5. Pavement Rehabilitation
  - Brooktree, Cherrywood, Majestic Way
  - Piedmont Drop-Off Area (projected)





			C	O	nst	tru	cti	on	P	roj	jec	ts	- 2	20	16											
	July				August			Septembe							November					December						
	1	We	ek 3	4	1	2	<u>Wee</u>	<u>k</u> 4	5	1	W€	eek 3	4	1		eek 3	4	1	2	<u> </u>	k 4	5	1	2	eek 3	4
Central Kitchen Demolition	'		3	4	'		3	4	5	ı		3	4	ı		3	4	'		3	4	5	'	2	3	4
Central Kitchen Construction																										
Central Kitchen Equipment																										
Sierramont Chiller Upgrade																										
Sierramont FIS/Modernization																										
Noble FIS/Modernization																										
Northwood FIS/Modernization																										
Summerdale FIS/Modernization																										
Vinci Park/Modernization																										
Paving Rehabilitation																										
Solar Project																										
Furniture																										
Carpet																										
Phase II Technology Upgrade																										$\sqsubset$
						Orc Bid	dere	d																		
							ard	⊥ Proi∈	ect																	
									neeri	ing																
							ving																			
							nstru																			
									Item																	
						Del	iver	Fur	nitur	^e																



Thank You
