
Berryessa Union School District Measure L Bond Construction Program


Board of Trustees' Update

Introduction

The following presentation is intended to provide the Board of Trustees with an update on the progress of Measure L Construction Bond Projects. These are projects that are currently active throughout the District.

Current Overall Project Status (presented 7/14/2015)

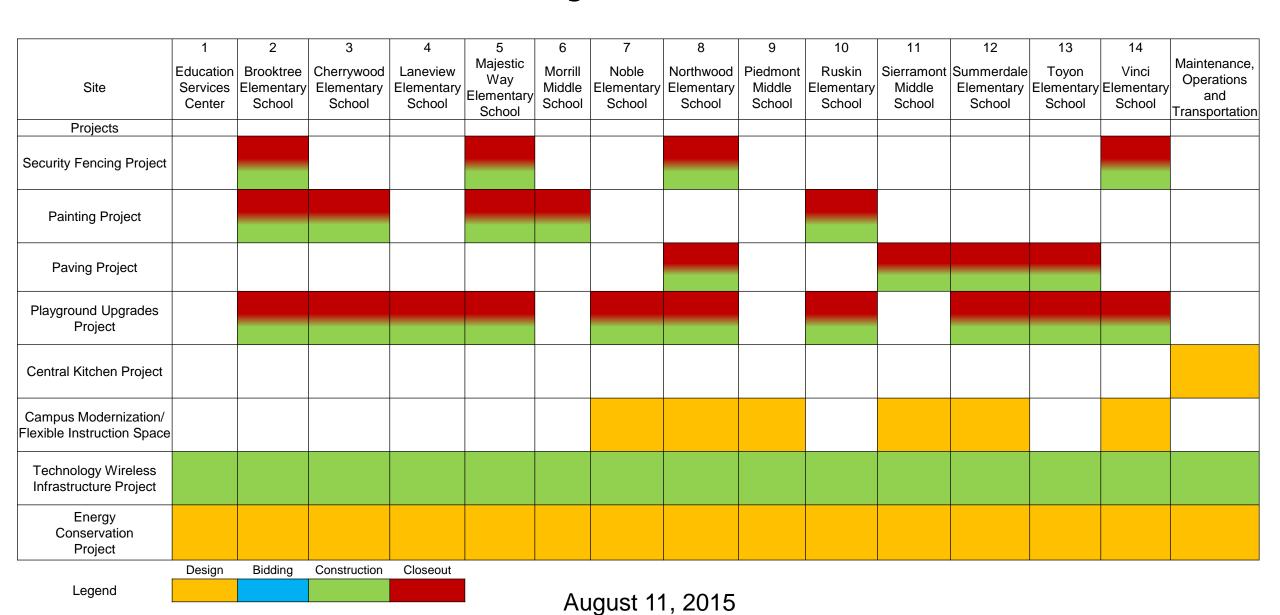


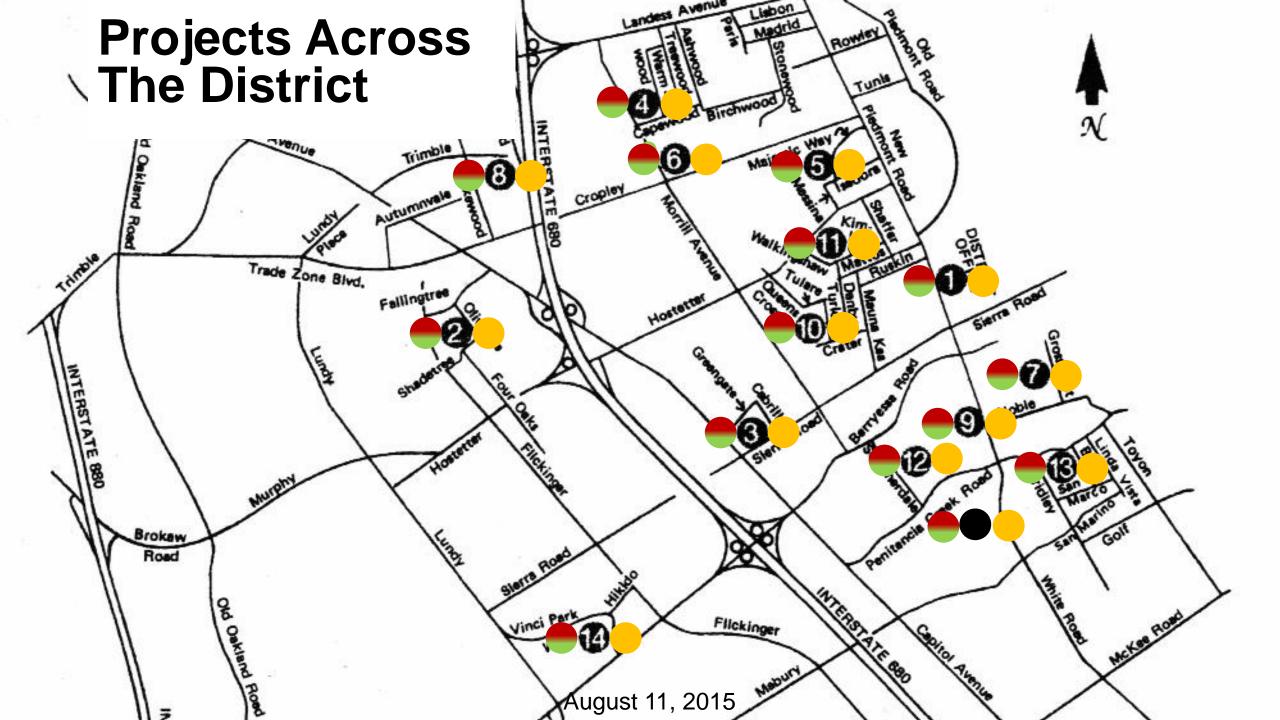

Current Overall Project Status


Legend

· · · · · · · · · · · · · · · · · · ·	1	2	3	4	5	6	7	8	9	10	11	12	13	14	
Site		Brooktree Elementary School	Cherrywood Elementary School	Laneview Elementary School	Majestic Way Elementary School	Morrill Middle School		Northwood Elementary School		t Ruskin Elementary School			Toyon Elementary School	Vinci y Elementary School	Maintenance, Operations and Transportation
Projects		<u> </u>			<u> </u>										
Security Fencing Project															
Painting Project															
Paving Project															
Playground Upgrades Project															
Central Kitchen Project		,			,										
Campus Modernization/ Flexible Instruction Space															
Technology Wireless Infrastructure Project															
Energy Conservation Project															
Waterline Replacement															
Pavement Rehabilitation for Athletic Courts															
	Design	Bidding	Construction	Closeout							•				

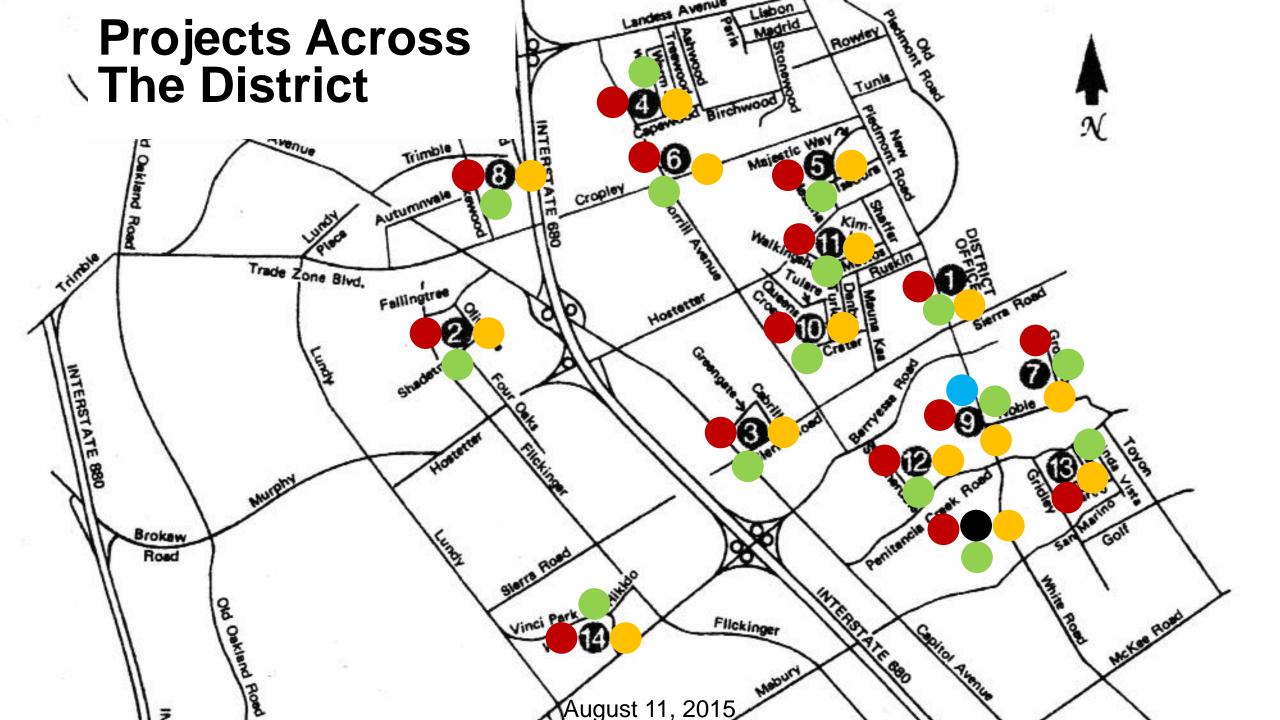


Brooktree ES

Replace fiber fall material and equipment





Cherrywood ES

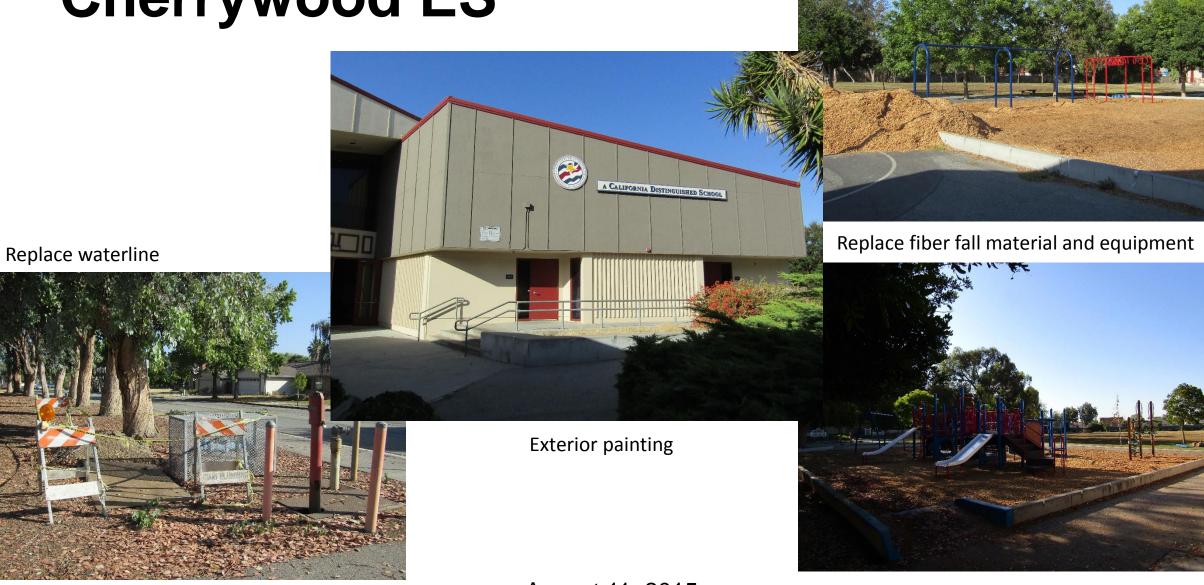

Laneview ES



Replace fiber fall material and equipment construction will be completed prior to start of school.

Majestic Way ES

Exterior painting



Replace fiber fall material and equipment

Noble ES



Replace fiber fall material and equipment construction will be completed prior to start of school.


Northwood ES





Replace fiber fall material and equipment



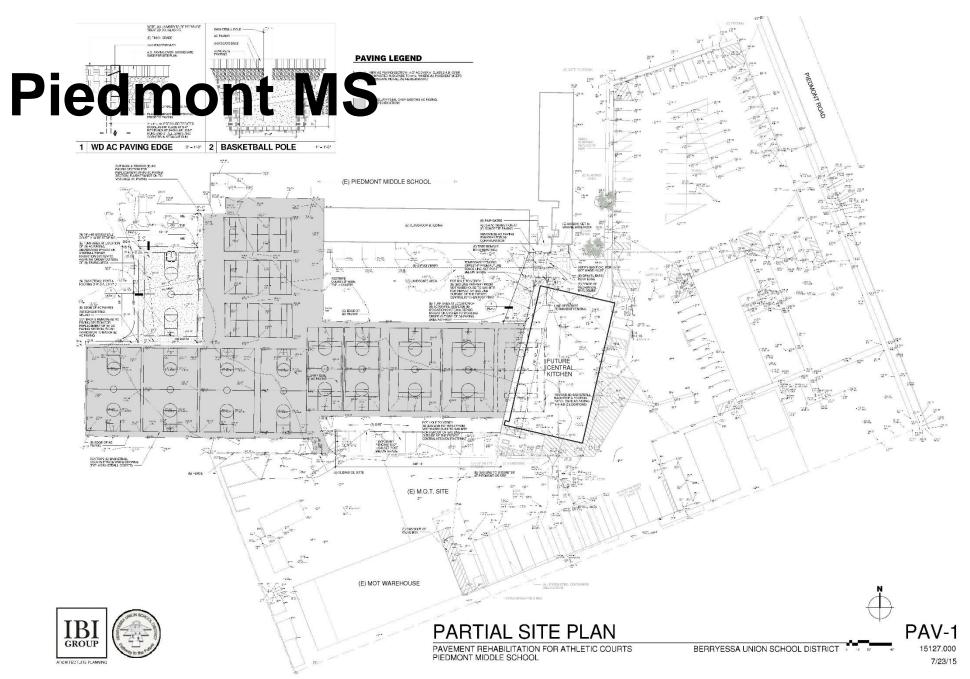

August 11, 2015

Ruskin ES



Exterior painting

Replace fiber fall material and equipment

Morrill Middle School



Sierramont MS



Summerdale ES






Replace fiber fall material and equipment

Toyon ES

Paving








Vinci Park ES







Security Fencing



Berryessa Union School District Measure L Bond Construction Program

LAN Network Upgrade Project

Technology Wireless LAN Upgrade Project



District Office
Data Center




Technology Wireless LAN Upgrade Project



District Office
Data Center

•

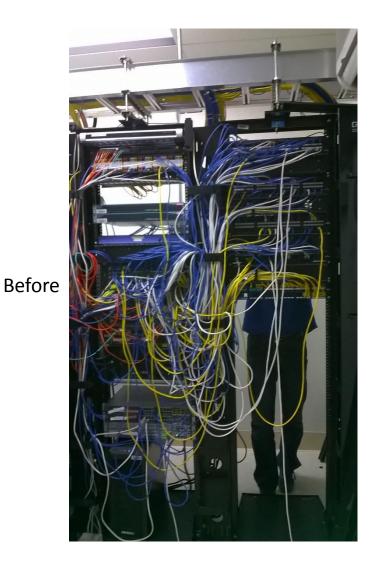


Technology Wireless LAN Upgrade Project





District Office cabling

Technology Wireless LAN Upgrade Project

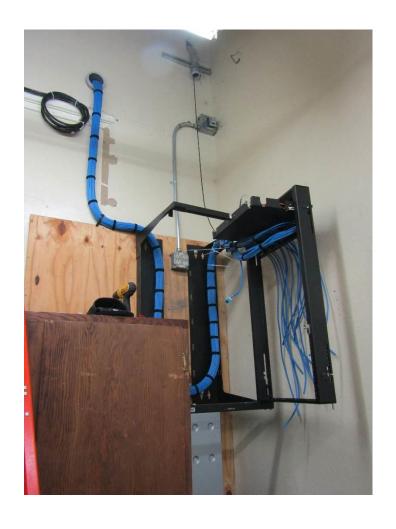

Sierramont MS cabling



LAN Network Upgrade Project - Phase I



The prior Megabits Per Second (mbps) was approximately 10 mbps with the equipment replacement it went to approximately 94 mbps. With the work completed at the Data Center and throughout the District Office, we are now realizing approximately 213 mbps.

Energy Conservation Project




Present Recommendation to Board of Trustees September 15,2015

Current Overall Project Status

Legend

	1	2	3	4	5	6	7	8	9	10	11	12	13	14	
Site		Brooktree Elementary School	Cherrywood Elementary School	Laneview Elementary School	Majestic Way Elementary School	Morrill Middle School	Elementary	Northwood Elementary School		t Ruskin Elementary School			Toyon Elementary School	Vinci y Elementary School	Maintenance, Operations and Transportation
Projects															
Security Fencing Project															
Painting Project															
Paving Project		!													
Playground Upgrades Project															
Central Kitchen Project															
Campus Modernization/ Flexible Instruction Space															
Technology Wireless Infrastructure Project															
Energy Conservation Project															
Waterline Replacement		!													
Pavement Rehabilitation for Athletic Courts															
	Design	Bidding	Construction	Closeout					•						

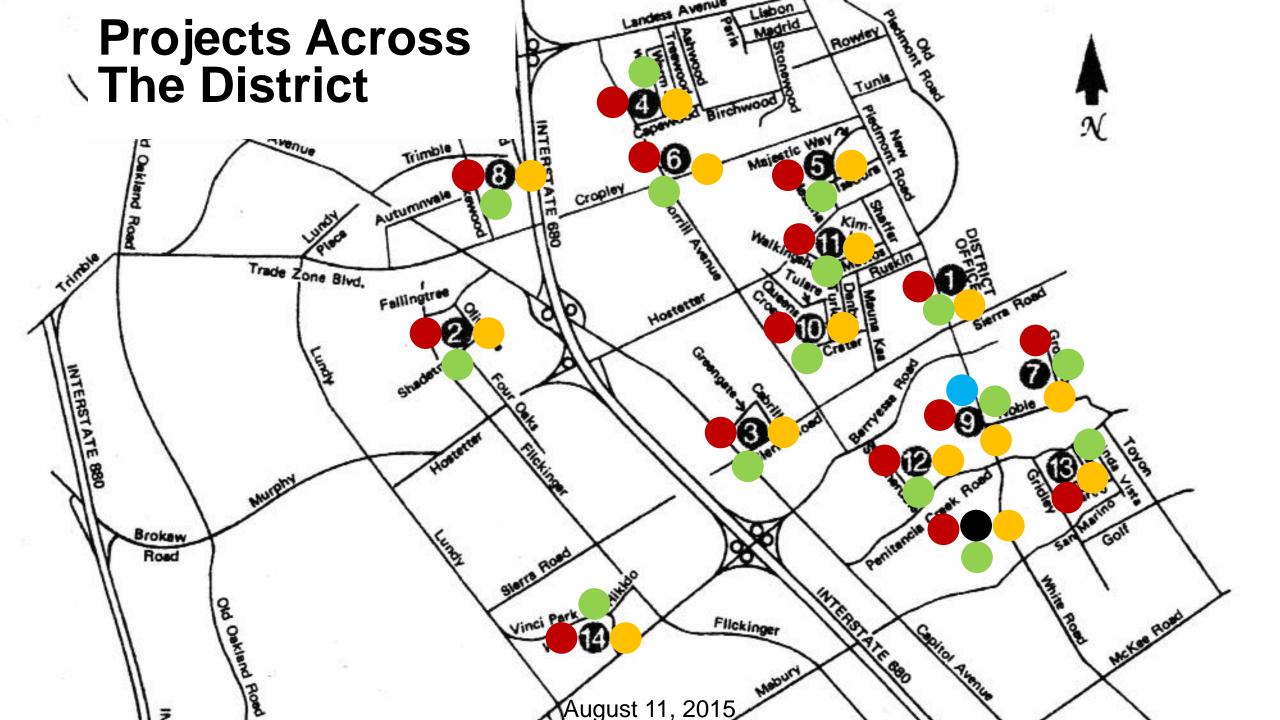

Measure L Bond Signage

Measure L

Bond Construction Program

Berryessa Union School District

Thanks Our Community
For All Our Kids, All Our Schools


Superintendent Will H. Ector, Jr.

Deputy Superintendent Phuong Le

www.berryessa.k12.ca.us

Board of Trustees

Thelma Boac Hugo Jimenez Richard Claspill David Cohen Khoa Nguyen

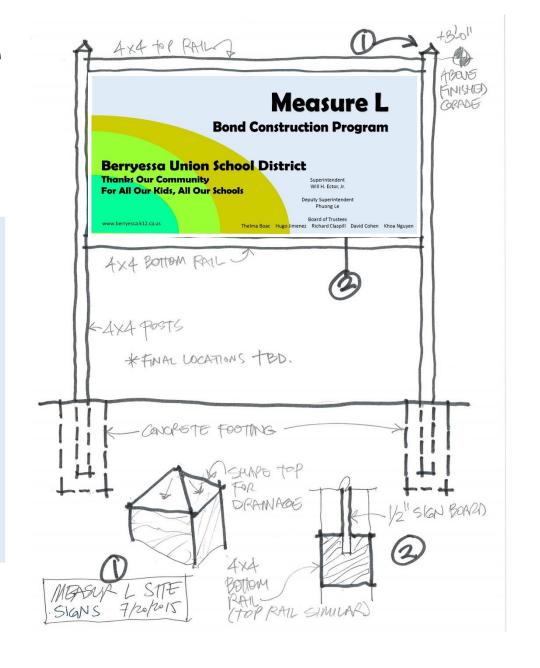

Measure L Bond Program Web Site is active but under Continuous Improvement

Berryessa Union School District - Bond Measures



Measure L Bond Construction

Berryessa Union School District

Thanks The Community!

Northwood Elementary School

2760 Trimble Ave.

San Jose, CA 95132

August 17, 2015

9:30am - 10:30am

Berryessa Union School District

Measure L Bond Construction Program

Thank You
